


Main Milestone Overview(M0,M1,S25,DS,M3)

15-May-06 16:45


◆ = M1 Target ▼ = Current Target --/- = Calculated finish

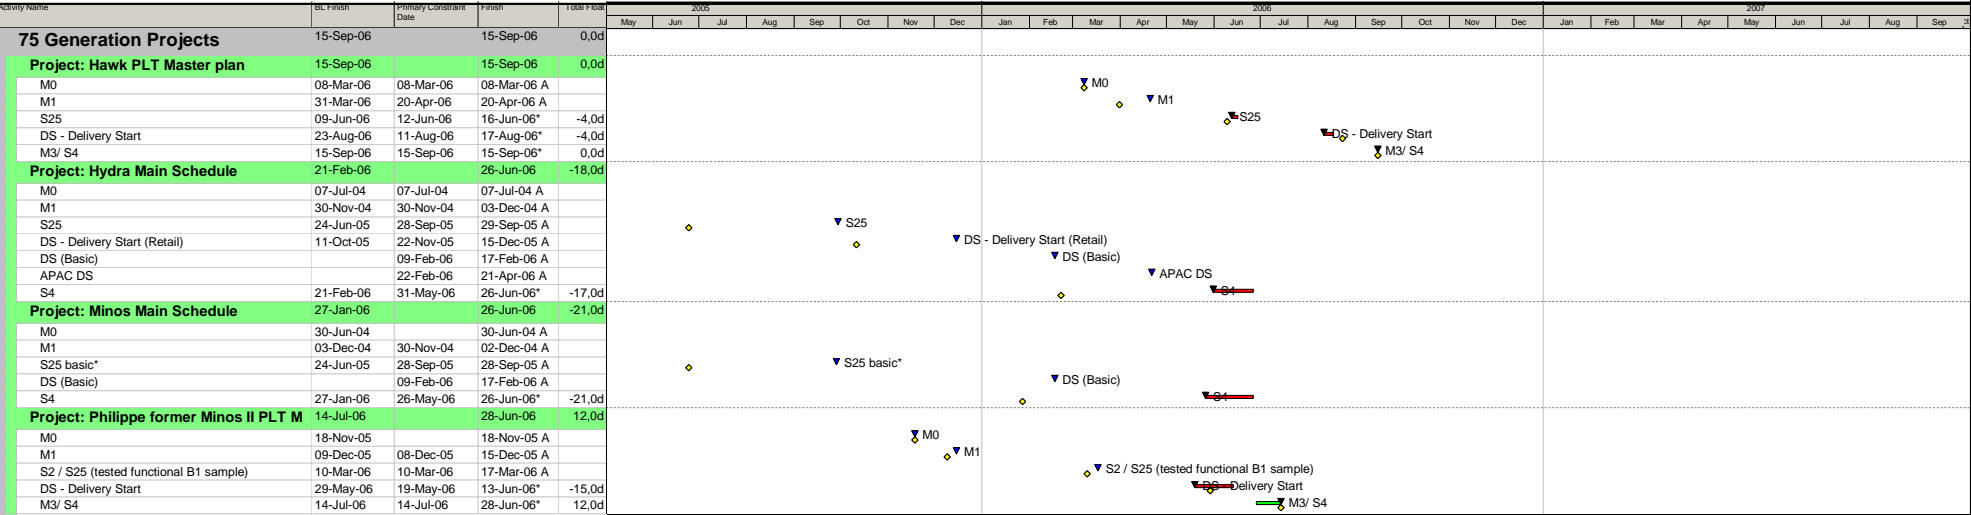

Main Milestone Overview(M0,M1,S25,DS,M3)

15-May-06 16:45

◆ = M1 Target ▼ = Current Target --/-- = Calculated finish

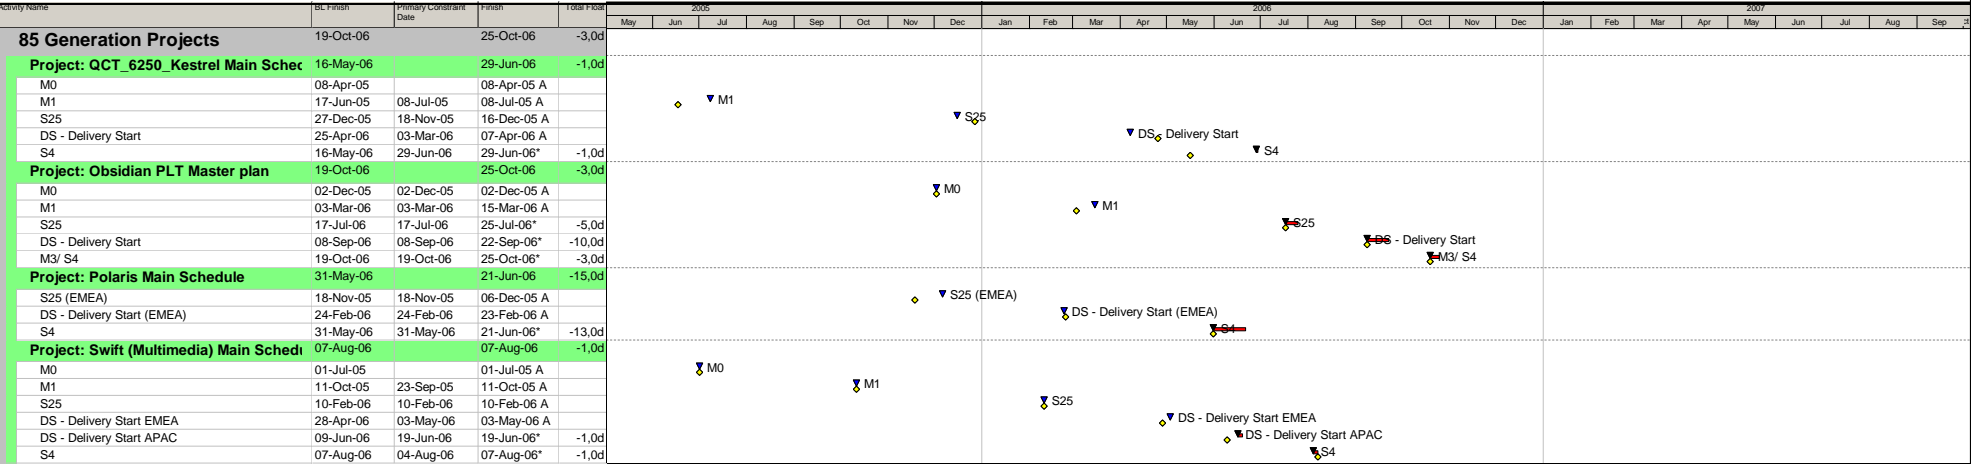

Main Milestone Overview(M0,M1,S25,DS,M3)

15-May-06 16:45

◆ = M1 Target ▼ = Current Target --/-- = Calculated finish

Activity Name	B/L Finish	Primary Constraint Date	Finish	Total Float	2005												2006												2007											
					May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec				
95 Generation Projects	11-Apr-07		11-Apr-07	0,0d																																				
Project: QCT_6250_Onyx PLT Master plan	21-Dec-06		21-Dec-06	0,0d																																				
M0	09-Jan-06		09-Jan-06 A																																					
M1	17-Mar-06	24-Feb-06	17-Mar-06 A																																					
S25	24-Jul-06	21-Jul-06	21-Jul-06*	0,0d																																				
DS - Delivery Start / German Retailer	20-Oct-06	20-Oct-06	20-Oct-06*	0,0d																																				
M3/ S4	21-Dec-06	21-Dec-06	21-Dec-06*	0,0d																																				
Project: QCT 6280 Ruby PLT Master plan	11-Apr-07		11-Apr-07	0,0d																																				
M0	22-Feb-06	22-Feb-06	03-Mar-06 A																																					
M1	10-May-06	17-May-06	17-May-06*	0,0d																																				
S25	02-Nov-06	04-Oct-06	04-Oct-06*	0,0d																																				
DS - Delivery Start		28-Feb-07		0,0d																																				
M3/S4	11-Apr-07	11-Apr-07	11-Apr-07*	0,0d																																				
