


Main Milestone Overview(M0,M1,S25,DS,M3)

07-Feb-06 17:02


◆ = M1 Target ▼ = Current Target - - / - - = Calculated finish

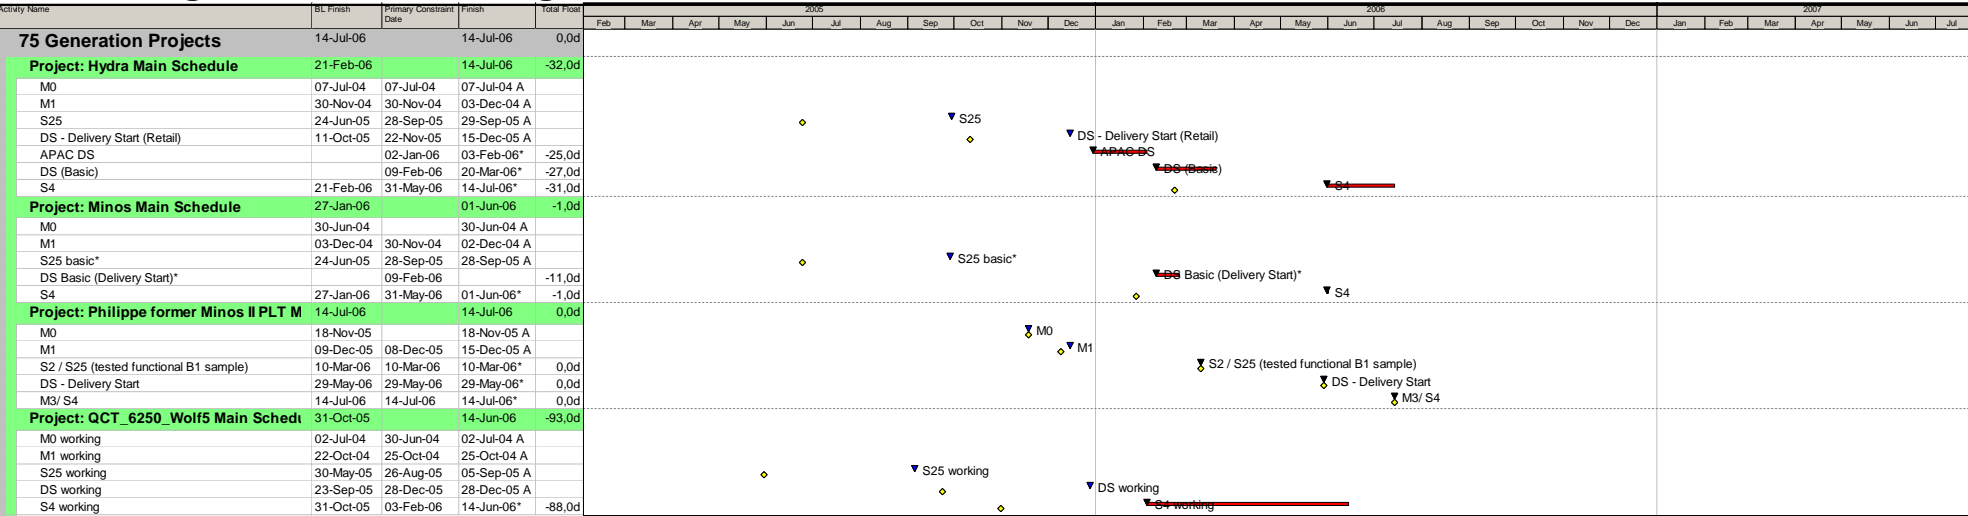

Main Milestone Overview(M0,M1,S25,DS,M3)

07-Feb-06 17:02

◆ = M1 Target ▼ = Current Target - - / - - = Calculated finish

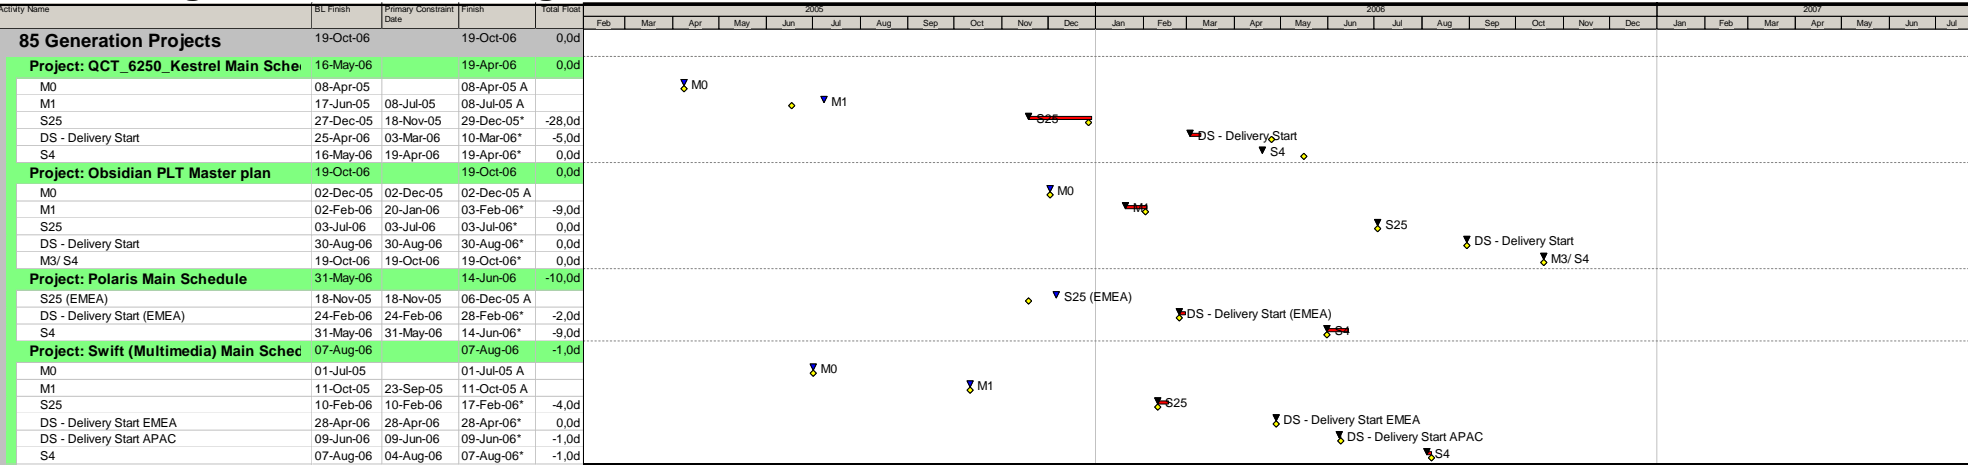

Main Milestone Overview(M0,M1,S25,DS,M3)

07-Feb-06 17:02

◆ = M1 Target ▼ = Current Target - - / - = Calculated finish

Activity Name	BL Finish	Primary Constraint Date	Finish	Total Float	2006												2006												2007											
					Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul						
95 Generation Projects					10-Nov-06	0,0d																																		
Project: QCT_6250_QCT_6250_Onyx P					10-Nov-06	0,0d																																		
M0			09-Jan-06 A		▼ M0																																			
M1			23-Mar-06*	-24,0d																																				
S25			04-Jul-06	04-Jul-06*	▼ S25																																			
DS - Delivery Start / German Retailer			20-Oct-06	20-Oct-06*	▼ DS - Delivery Start / German Retailer																																			
M3/ S4			10-Nov-06	10-Nov-06*	▼ M3/ S4																																			

