

ID		Task Name	Duration	Start	Finish	March					
						2/12	2/19	2/26	3/5	3/12	3/19
61		<b>Volume side key, Ringer side key and lock key in</b>	<b>4 wks</b>	<b>Mar 20 '06</b>	<b>Apr 14 '06</b>						
62		ringer side key in idle	2 wks	Mar 20 '06	Mar 31 '06						
63		volume side key in call	1 wk	Apr 3 '06	Apr 7 '06						
64		lock key	1 wk	Apr 10 '06	Apr 14 '06						
65		<b>Synchronization including remote sync and sync</b>	<b>5 wks</b>	<b>Mar 6 '06</b>	<b>Apr 7 '06</b>						
66		SyncML UI adaption	4 wks	Mar 6 '06	Mar 31 '06						
67		SyncML workflow adaption	5 wks	Mar 6 '06	Apr 7 '06						
68		<b>Settings</b>	<b>3 wks</b>	<b>Apr 3 '06</b>	<b>Apr 21 '06</b>						
69		ring tong, keypad tone, time/date	3 wks	Apr 3 '06	Apr 21 '06						
70		display my number, language, change PIN	3 wks	Apr 3 '06	Apr 21 '06						
71		Unified Inbox (Layout)	2 wks	Apr 3 '06	Apr 14 '06						
72		Templates/Drafts	4 wks	Mar 27 '06	Apr 21 '06						
73		<b>View contact log</b>	<b>4 wks</b>	<b>Mar 27 '06</b>	<b>Apr 21 '06</b>						
74		new msg info table support in PIM AE	4 wks	Mar 27 '06	Apr 21 '06						
75		sorting mechanism	4 wks	Mar 27 '06	Apr 21 '06						
76		UI implementation in PIM	4 wks	Mar 27 '06	Apr 21 '06						
77		export inteface (insert contact, select contact) to ex	4 wks	Mar 27 '06	Apr 21 '06						
78		call record adaption	4 wks	Mar 27 '06	Apr 21 '06						
79		<b>Remove or disable or hide features</b>	<b>4 wks</b>	<b>Mar 27 '06</b>	<b>Apr 21 '06</b>						
80		Irda, BT (remove)	2 wks	Apr 3 '06	Apr 14 '06						
81		Camera (remove)	2 wks	Apr 3 '06	Apr 14 '06						
82		Browser (hide)	4 wks	Mar 27 '06	Apr 21 '06						
83		showing UI notification about accessory from conne	2 wks	Apr 3 '06	Apr 14 '06						
84		customization	2 wks	Apr 10 '06	Apr 21 '06						
85		Development test and Sprint 2 ST	0.8 wks?	Apr 25 '06	Apr 28 '06						
86		<b>Feature Sprint 3</b>	<b>10.6 wks?</b>	<b>Mar 20 '06</b>	<b>May 31 '06</b>						
87		Key lock screen after switching the key lock hard key.	4 wks	Apr 24 '06	May 19 '06						
88		Inbox UI (all message list)	5 wks	Mar 27 '06	Apr 28 '06						
89		Settings complete	3 wks	Apr 24 '06	May 12 '06						
90		<b>Startup Assistant</b>	<b>6 wks</b>	<b>Apr 10 '06</b>	<b>May 19 '06</b>						

Project: Jerry SW Feature Planning 20  
Date: Feb 20 '06

Task



Milestone



External Tasks



Split



Summary



External Milestone



Progress

























Project Summary



Deadline





ID		Task Name	Duration	Start	Finish	March					
						2/12	2/19	2/26	3/5	3/12	3/19
121		DRM (disable)	4 wks	Apr 24 '06	May 19 '06						
122		<b>VF Simply Alarm Clock</b>	<b>4 wks</b>	<b>Apr 24 '06</b>	<b>May 19 '06</b>						
123		list all alarm events	4 wks	Apr 24 '06	May 19 '06						
124		customization	2 wks	May 12 '06	May 25 '06						
125		Development test and Sprint 3 ST	0.8 wks?	May 26 '06	May 31 '06						
126		<b>Feature Sprint 4</b>	<b>14.6 wks</b>	<b>Mar 20 '06</b>	<b>Jun 28 '06</b>						
127		Idle split screen	4 wks	Jun 1 '06	Jun 28 '06						
128		<b>Idle screen</b>	<b>12 wks</b>	<b>Mar 20 '06</b>	<b>Jun 9 '06</b>						
129		Welcome tour	1 wk	Jun 5 '06	Jun 9 '06						
130		Charging display adaption	1 wk	Jun 5 '06	Jun 9 '06						
131		<b>Interruption by Events</b>	<b>9.8 wks</b>	<b>Mar 20 '06</b>	<b>May 25 '06</b>						
132		Separation of Call functionality from the Idle	6 wks	Mar 20 '06	Apr 28 '06						
133		Call CSM Message Handling	6 wks	Apr 10 '06	May 19 '06						
134		Dial Dialog Updation Handling	4 wks	Apr 28 '06	May 25 '06						
135		<b>Sleep mode with timer settings</b>	<b>5 wks</b>	<b>May 22 '06</b>	<b>Jun 23 '06</b>						
136		back to last screen	4 wks	May 22 '06	Jun 16 '06						
137		screen saver handling in idle	2 wks	Jun 12 '06	Jun 23 '06						
138		<b>Text Message (SMS)</b>	<b>5.6 wks</b>	<b>May 8 '06</b>	<b>Jun 14 '06</b>						
139		view and editor	5 wks	May 8 '06	Jun 9 '06						
140		send and receive	2 wks	Jun 1 '06	Jun 14 '06						
141		<b>hover functionality in Contact list</b>	<b>4 wks</b>	<b>May 22 '06</b>	<b>Jun 16 '06</b>						
142		Implementation by UIOS	2 wks	May 22 '06	Jun 2 '06						
143		PIM Adaption	2 wks	Jun 5 '06	Jun 16 '06						
144		messaging adaption	2 wks	Jun 5 '06	Jun 16 '06						
145		<b>VF Simply Alarm Clock</b>	<b>3 wks</b>	<b>May 29 '06</b>	<b>Jun 16 '06</b>						
146		time/date editor	2 wks	May 29 '06	Jun 9 '06						
147		alarm text	1 wk	May 29 '06	Jun 2 '06						
148		alarm tone/volume/vibration	3 wks	May 29 '06	Jun 16 '06						
149		menu options in alarm clock, i.e. delete, add	2 wks	Jun 1 '06	Jun 14 '06						
150		Unified Inbox Functionality	6 wks	May 1 '06	Jun 9 '06						

Project: Jerry SW Feature Planning 20  
Date: Feb 20 '06

Task



Milestone



External Tasks



Split



Summary



External Milestone



Progress











Project Summary



Deadline




ID		Task Name	Duration	Start	Finish	March					
						2/12	2/19	2/26	3/5	3/12	3/19
151		Unified sent message	3 wks	May 29 '06	Jun 16 '06						
152		Delete (All) wizard	4 wks	May 29 '06	Jun 23 '06						
153		<b>MsgAE</b>	<b>3 wks</b>	<b>Jun 1 '06</b>	<b>Jun 21 '06</b>						
154		Sync between message table in PIM and message C	3 wks	Jun 1 '06	Jun 21 '06						
155		customization	3 wks	Jun 5 '06	Jun 23 '06						
156		Development test and Sprint 4 ST	1 wk?	Jul 3 '06	Jul 7 '06						
157		S25 SW bugfix	4 wks?	Jul 3 '06	Jul 28 '06						
158		<b>System Test</b>	<b>3 wks</b>	<b>Jul 3 '06</b>	<b>Jul 21 '06</b>						
159		1st full run	3 wks	Jul 3 '06	Jul 21 '06						


Project: Jerry SW Feature Planning 20  
Date: Feb 20 '06


Task

Split

Progress










Milestone

Summary

Project Summary








External Tasks


External Milestone


Deadline








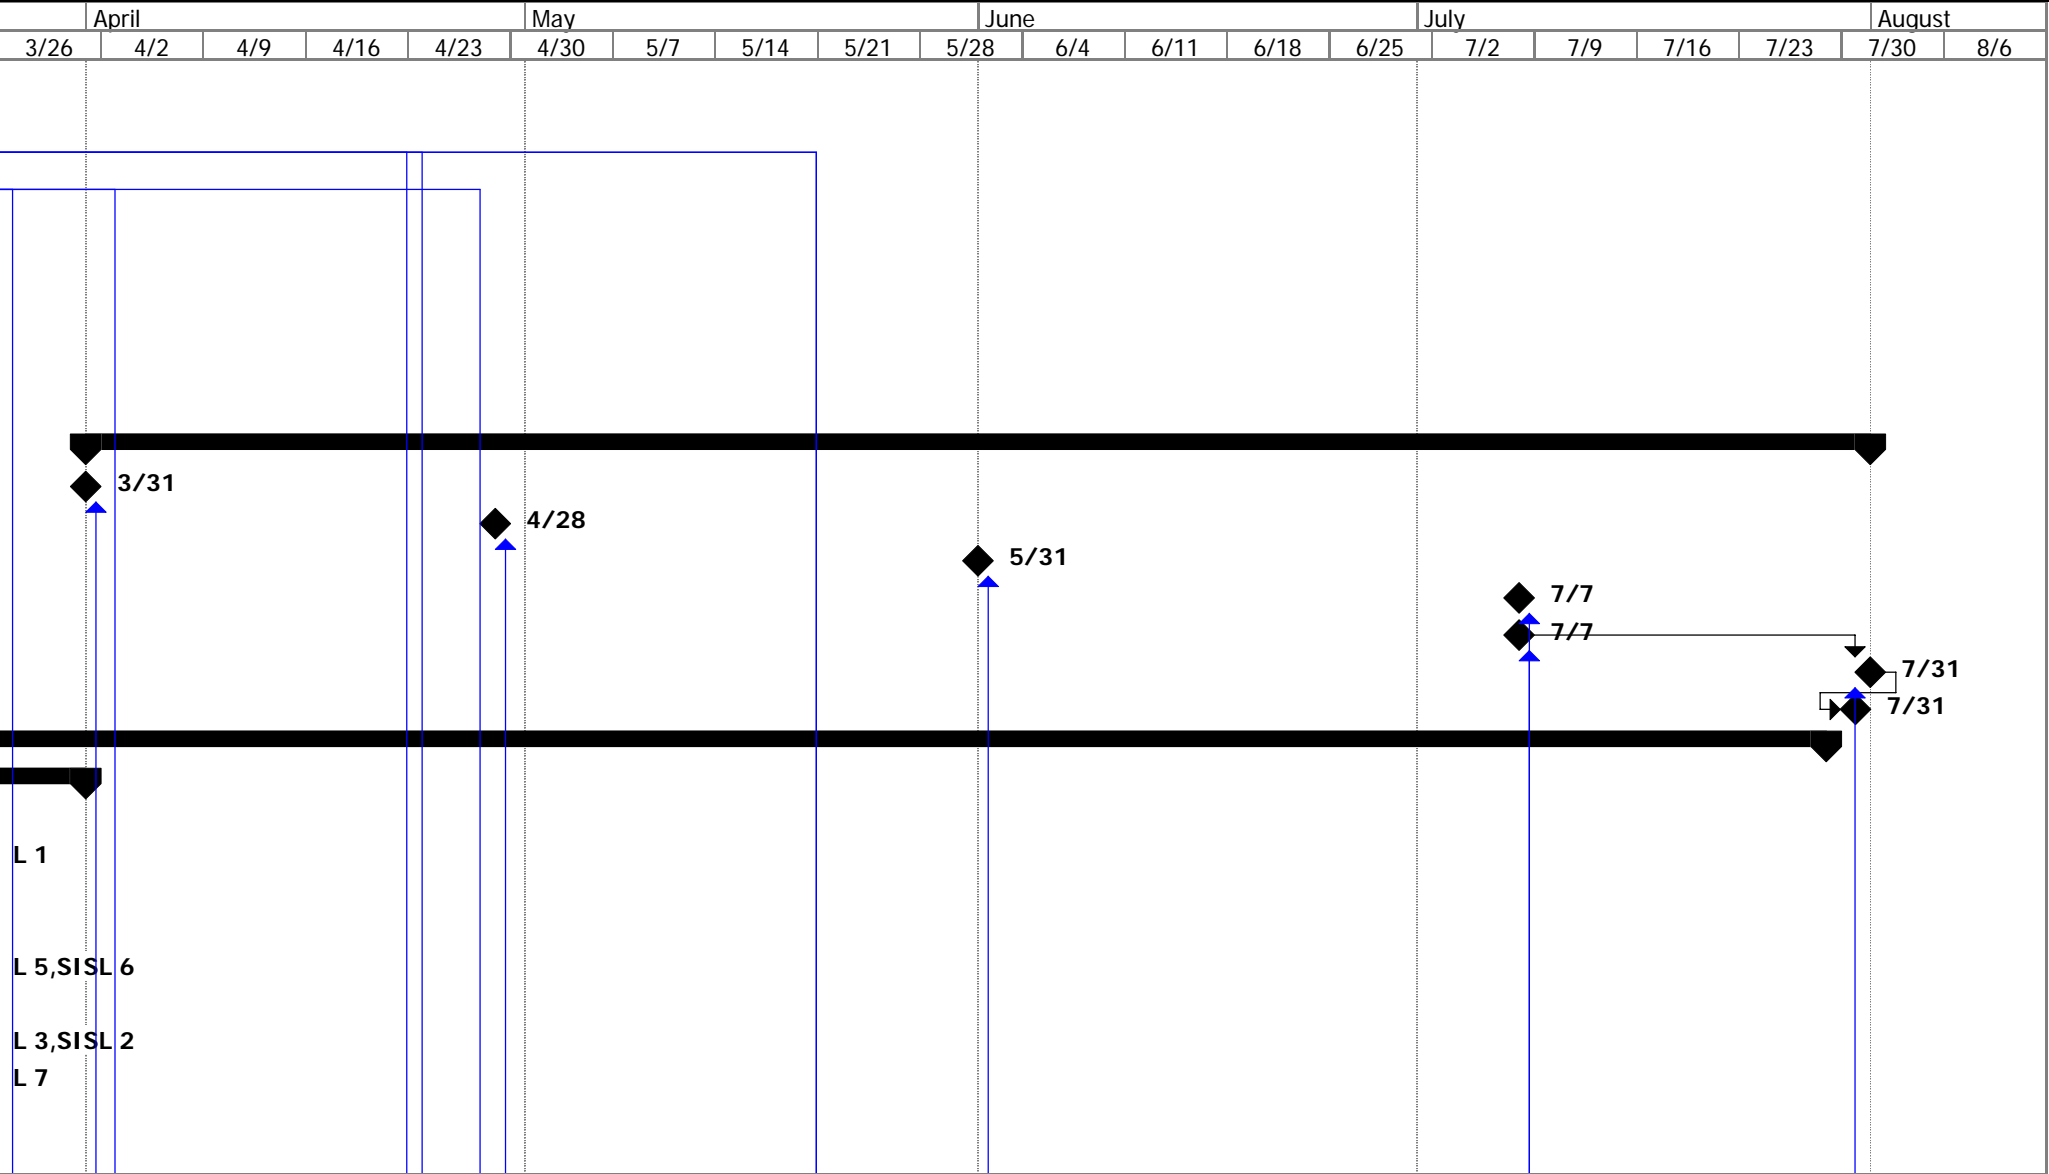

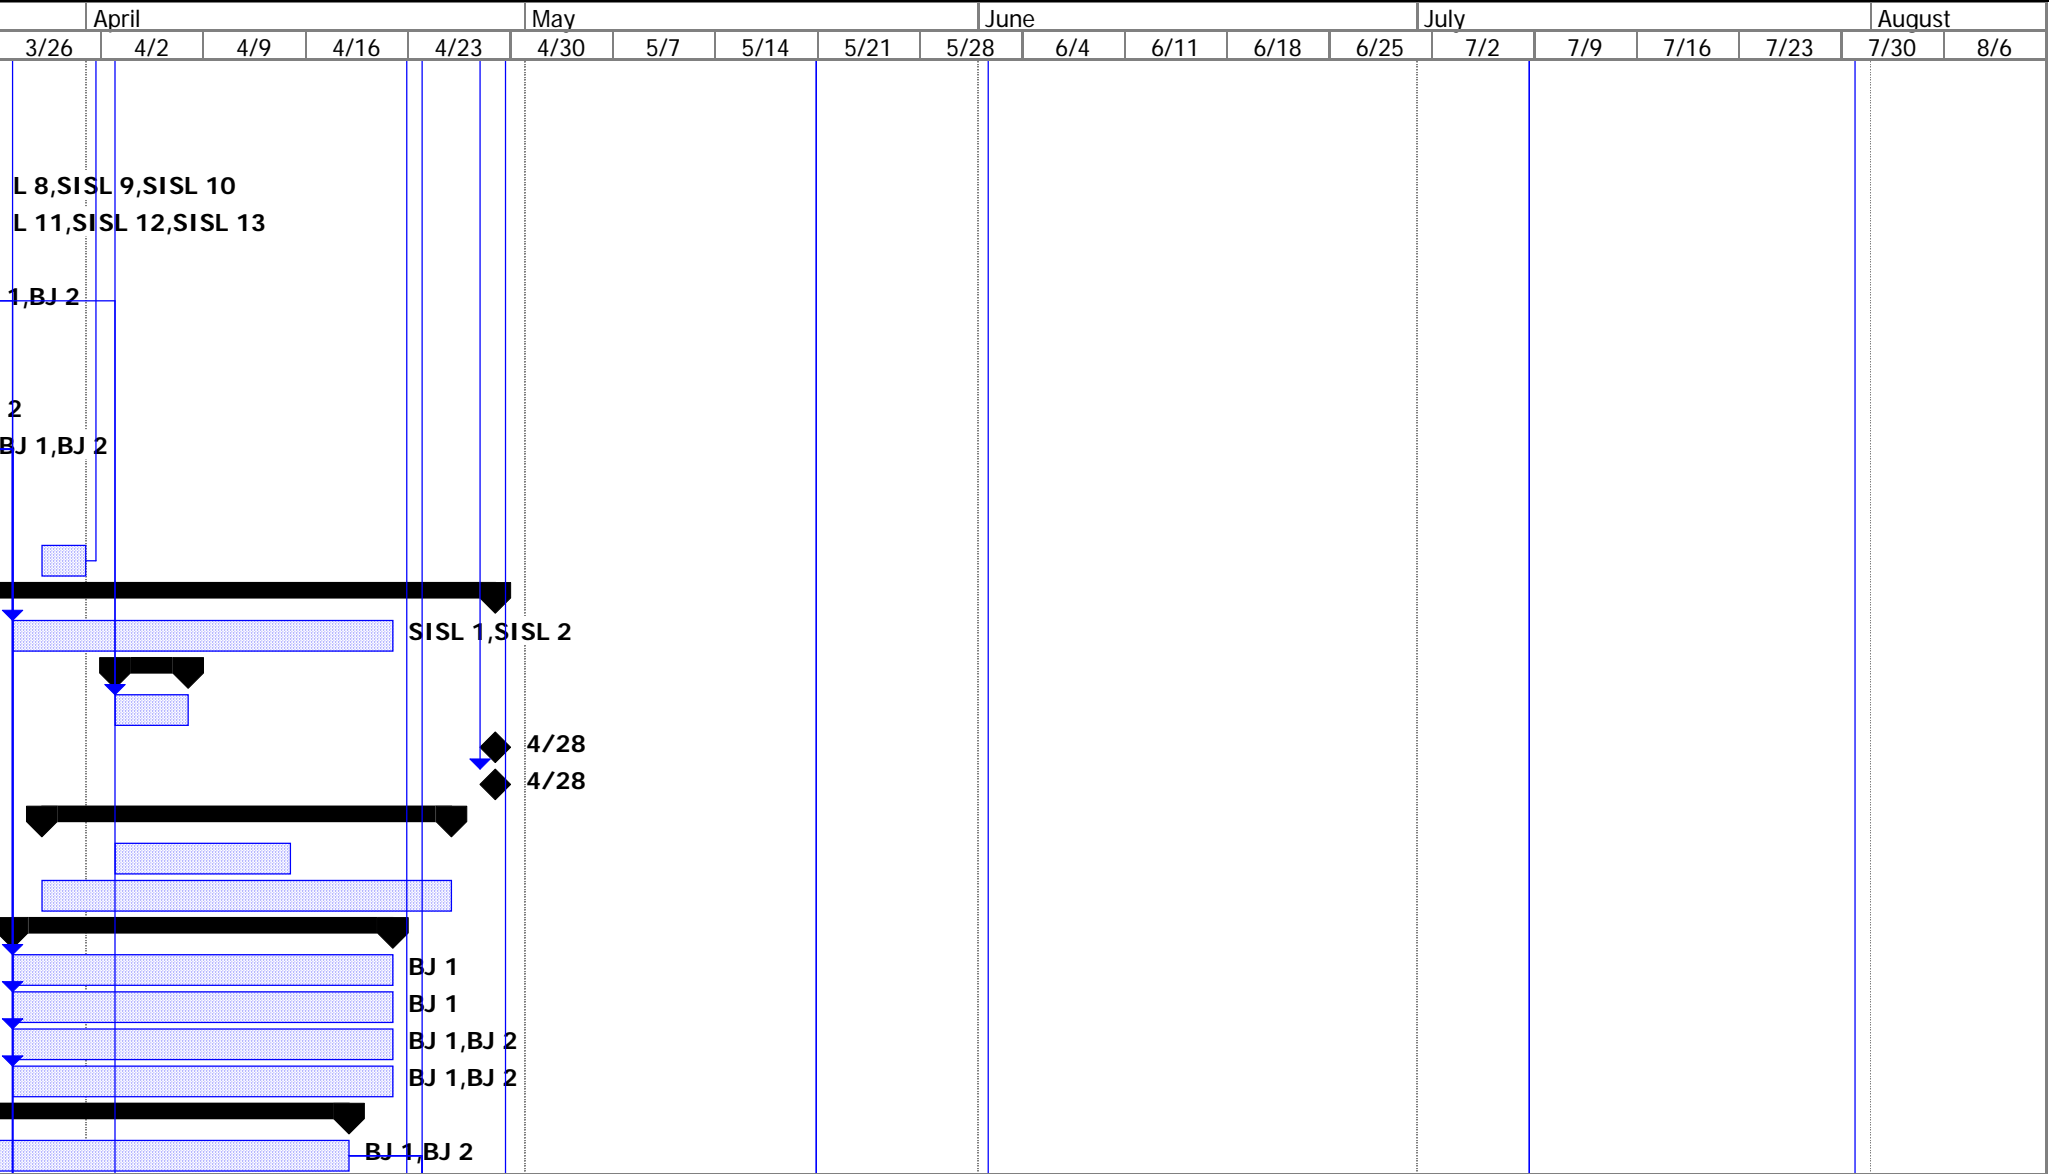



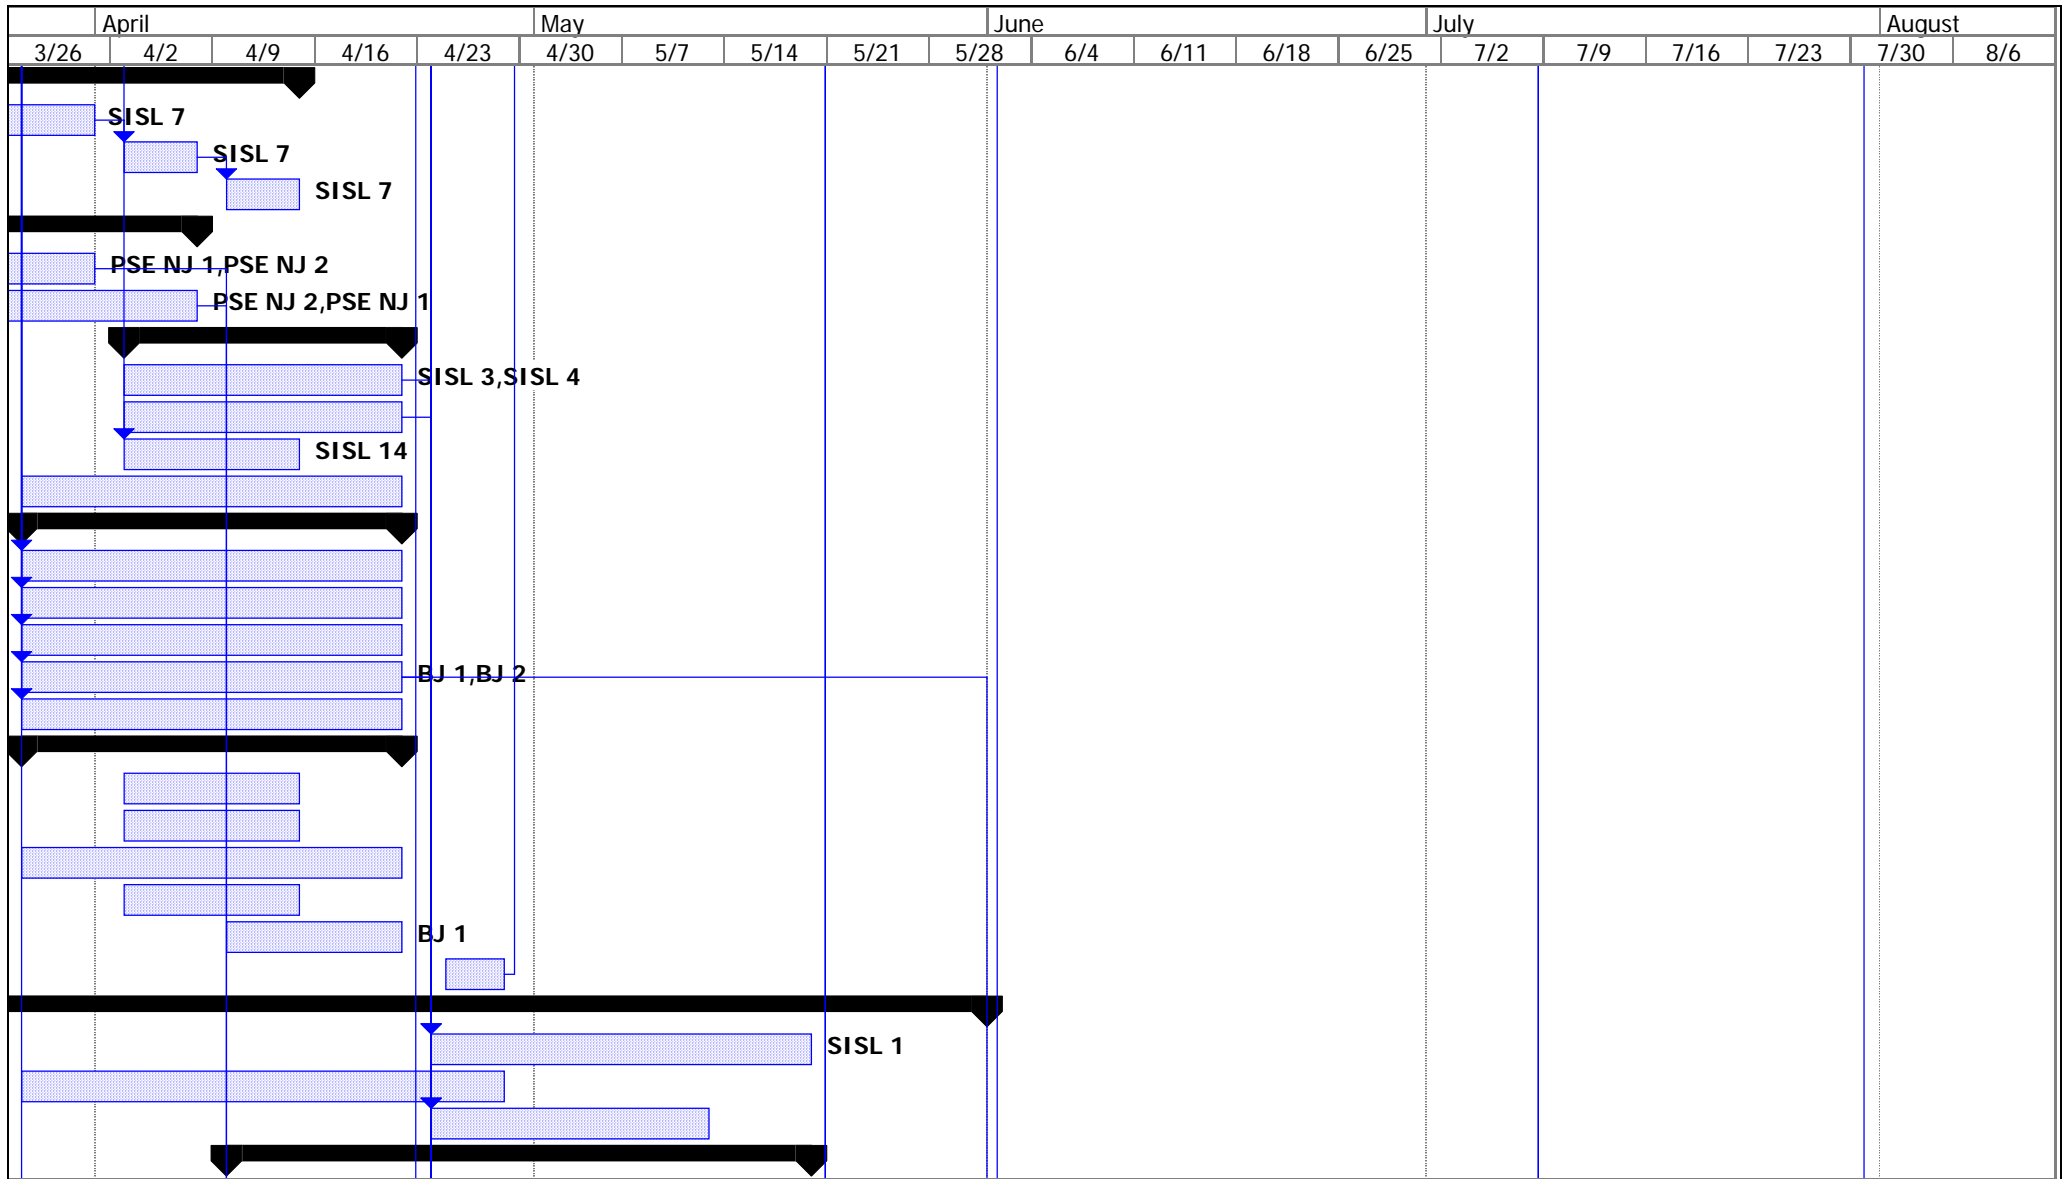

Project: Jerry SW Feature Planning 20  
Date: Feb 20 '06

Task

Split


Progress

Milestone  
Summary  
Project Summary

External Tasks

External Milestone

Deadline

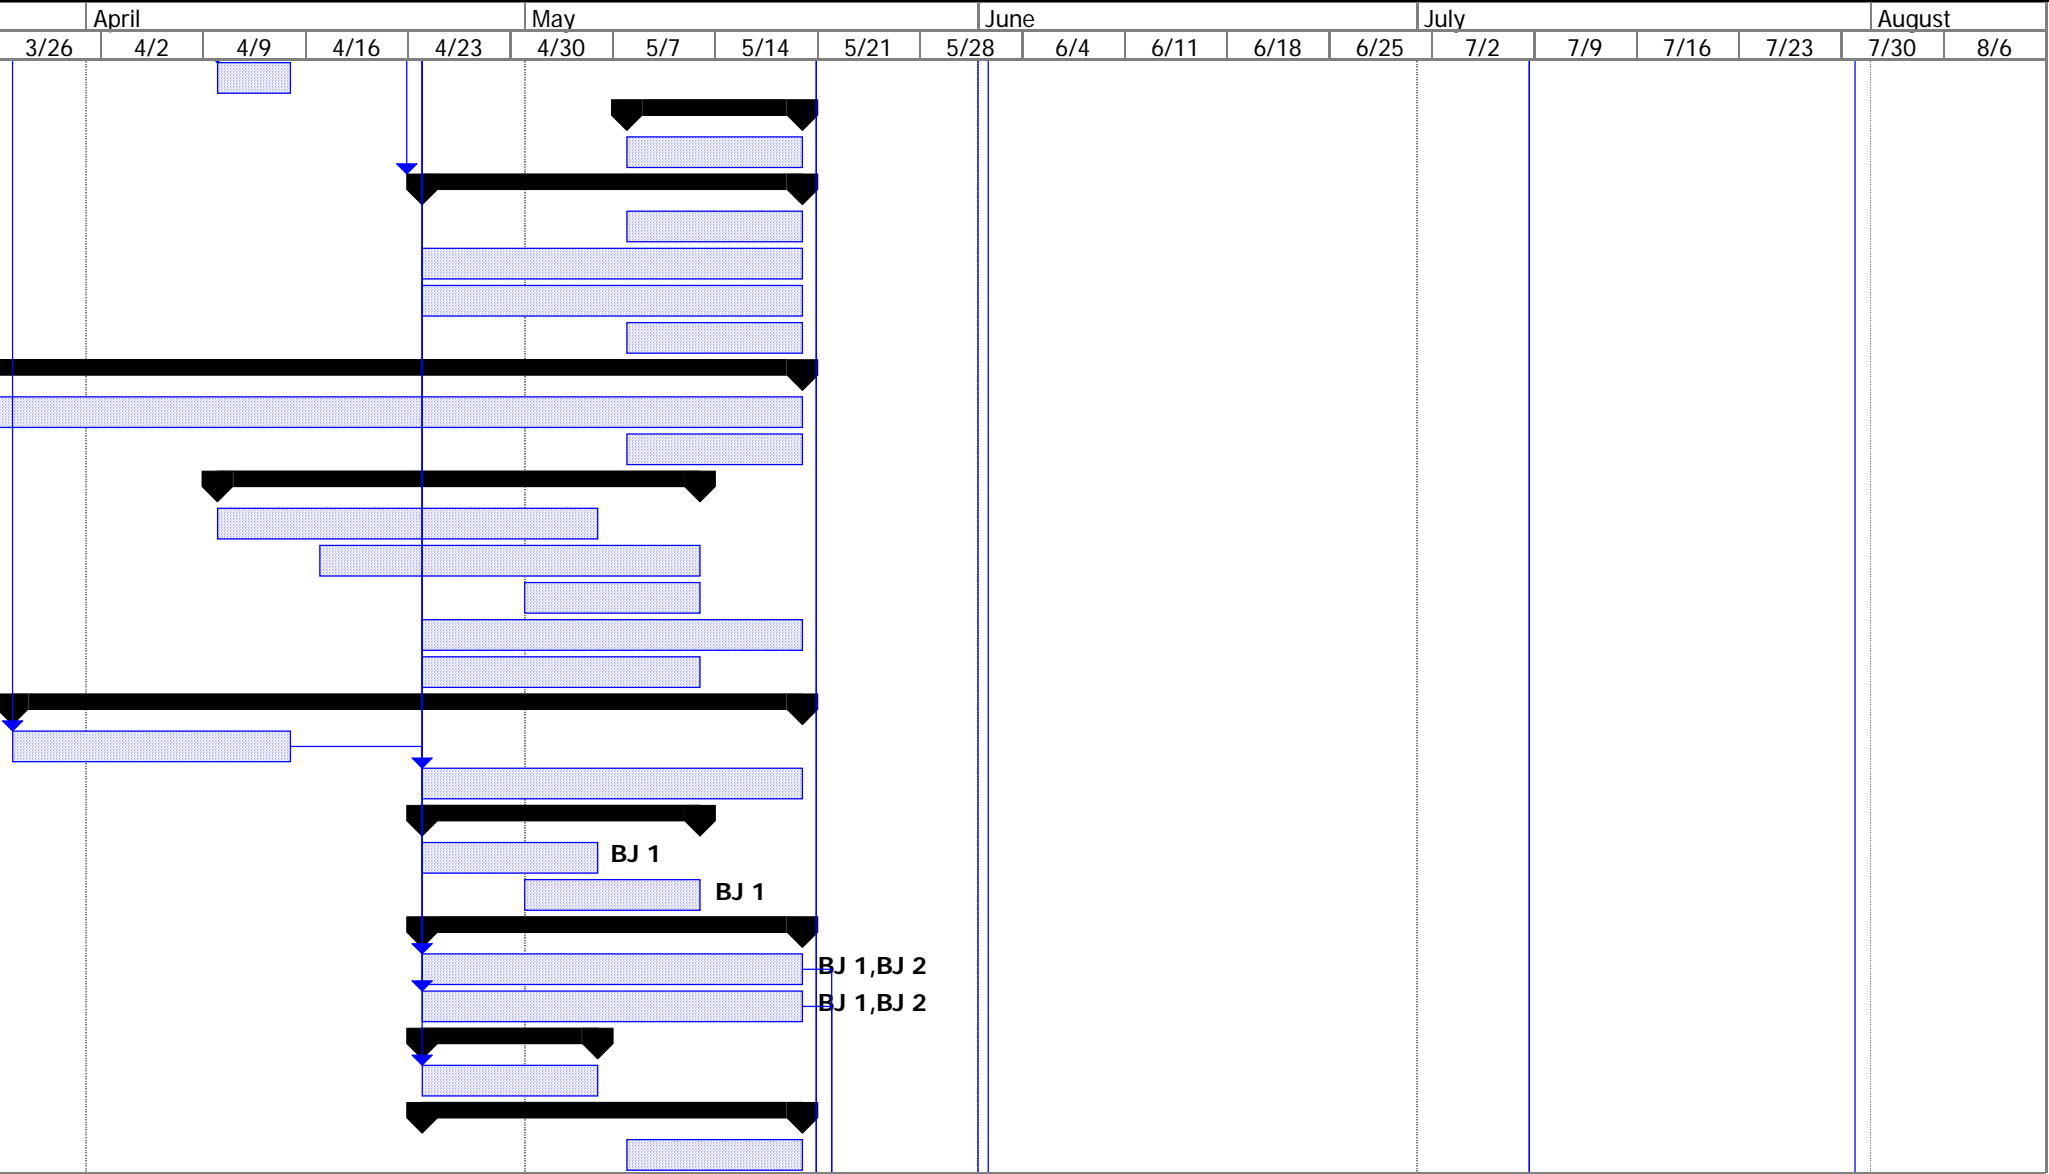

Project: Jerry SW Feature Planning 20  
Date: Feb 20 '06

Task

Split

Progress

Milestone


Summary

Project Summary

External Tasks

External Milestone

Deadline

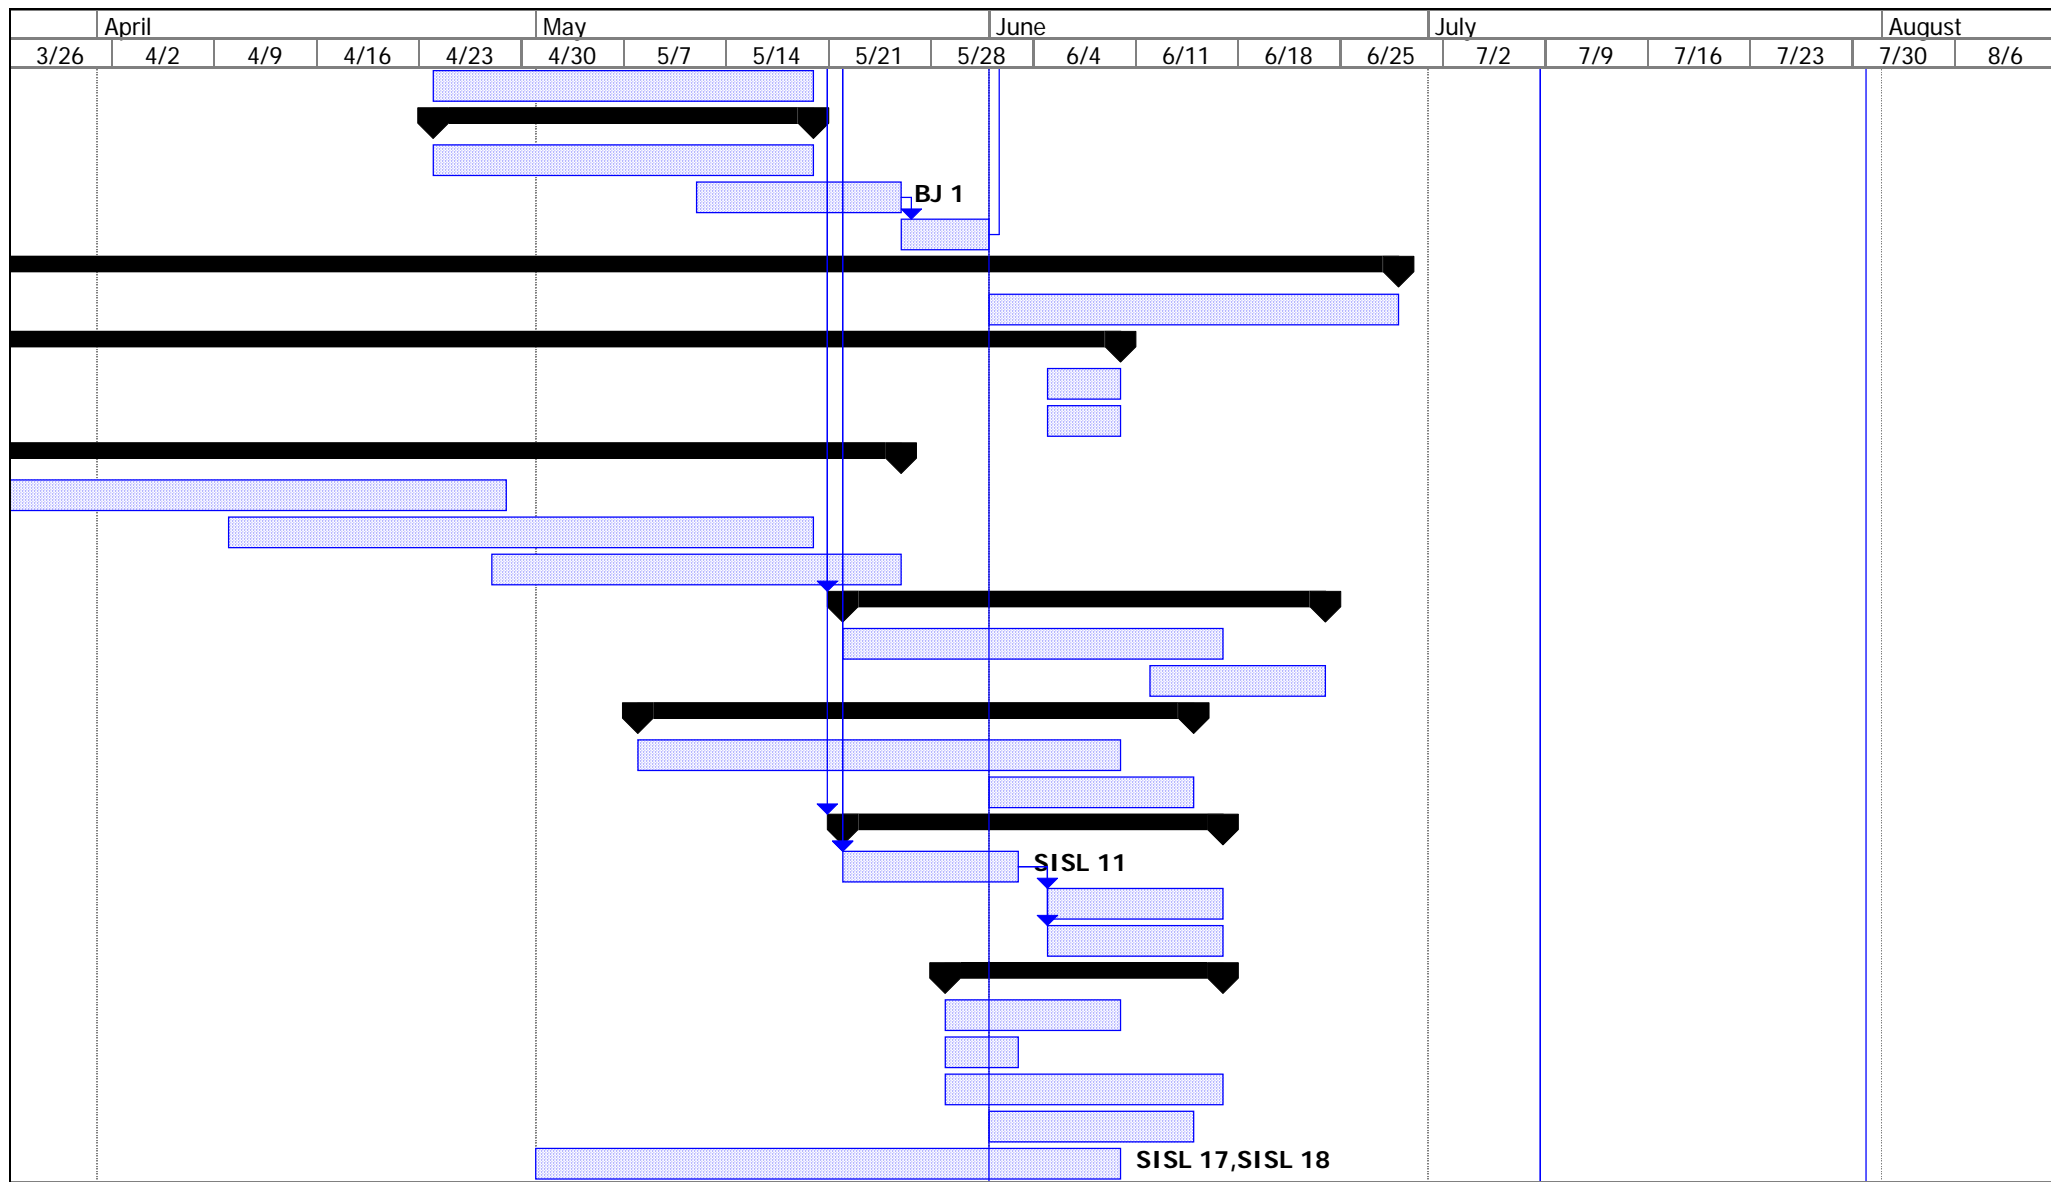

Project: Jerry SW Feature Planning 20  
Date: Feb 20 '06

## Task



## Milestone



## External Tasks



Split



## Summary



### External Milestone



## Progress




## Project Summary



Deadline



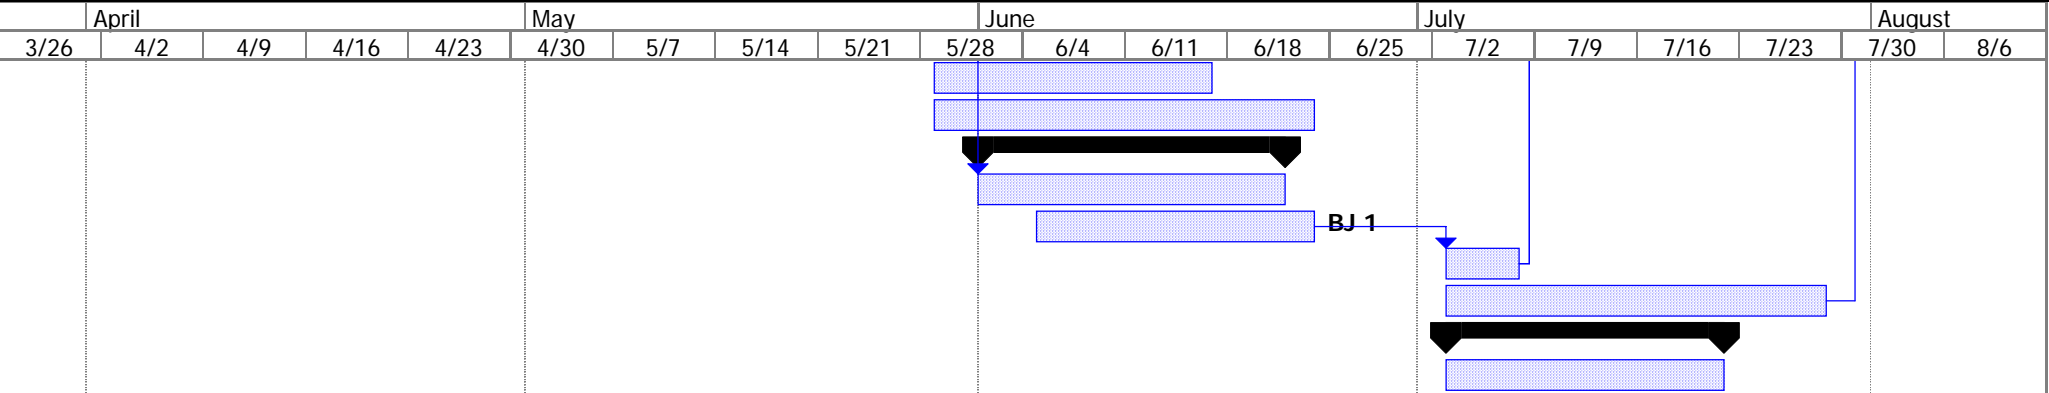



Project: Jerry SW Feature Planning 20  
Date: Feb 20 '06


Task

Split

Progress










Milestone

Summary

Project Summary







External Tasks

External Milestone

Deadline

