


Main Milestone Overview(M0,M1,S25,DS,M3)

07.02.06 14:47


◆ = M1 Target ▼ = Current Target - - / - = Calculated finish

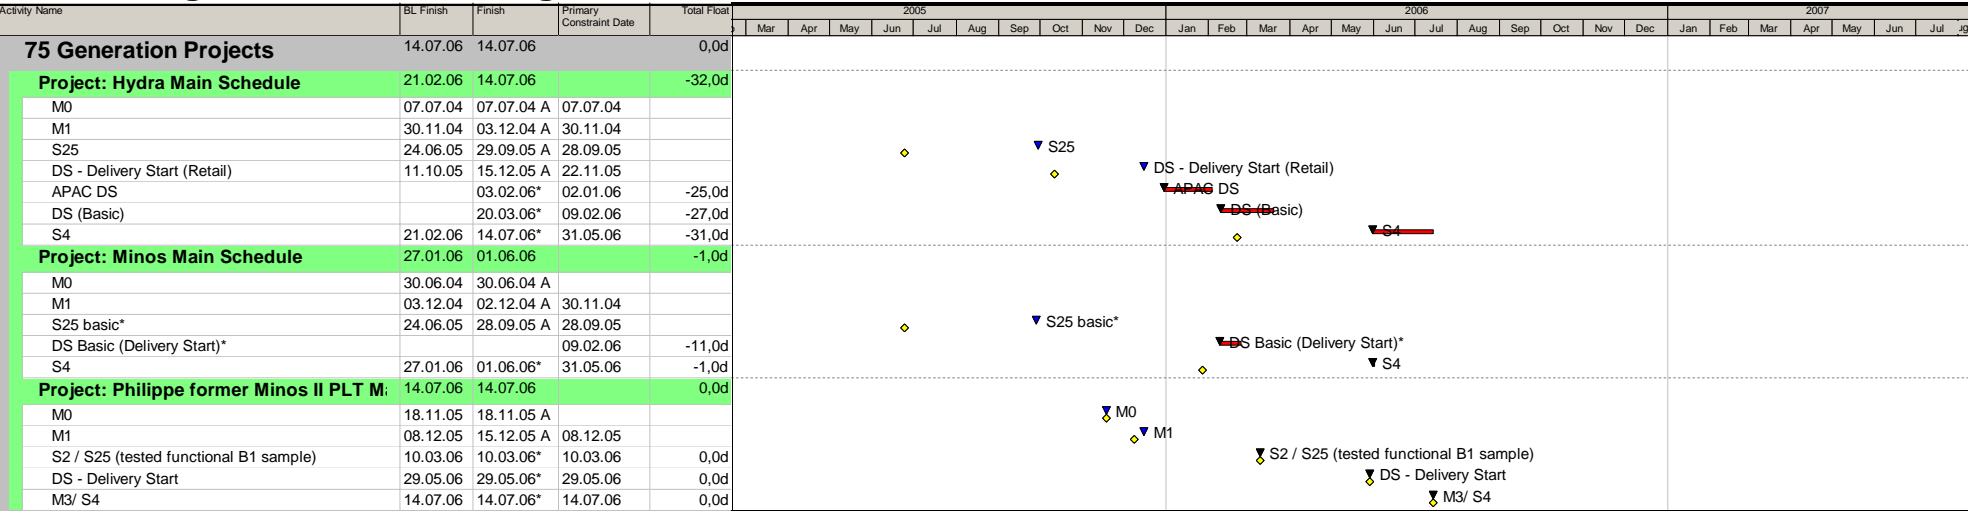

Main Milestone Overview(M0,M1,S25,DS,M3)

07.02.06 14:47

◆ = M1 Target ▼ = Current Target - - / - = Calculated finish

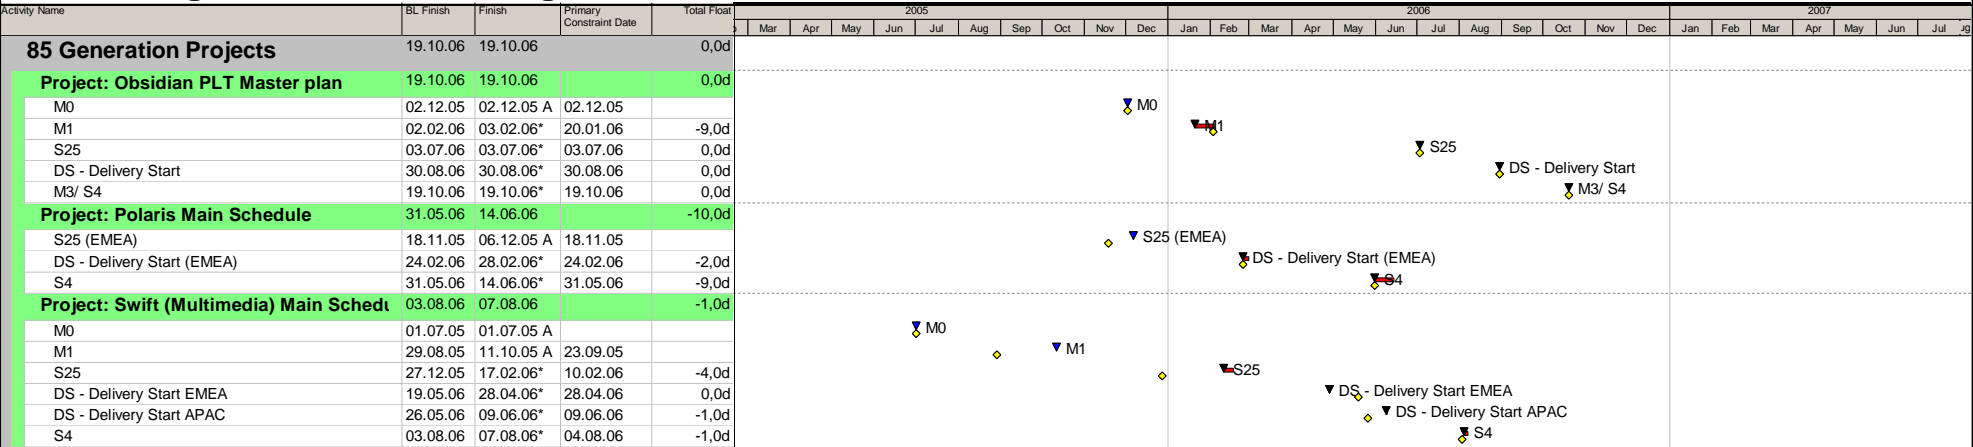

Main Milestone Overview(M0,M1,S25,DS,M3)

07.02.06 14:47

◆ = M1 Target ▼ = Current Target -/- = Calculated finish

Activity Name	BL Finish	Finish	Primary Constraint Date	Total Float	2005												2006												2007													
					Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec				
95 Generation Projects	28.03.07	28.03.07		0,0d																																						
Project: X95_MP-E+_SG3_Diamond TPM	28.03.07	28.03.07		0,0d																																						
M0	08.03.06	08.03.06*	08.03.06	0,0d													▼ M0																									
M1	18.05.06	18.05.06*	10.05.06	-6,0d													▼ M1																									
S25	03.11.06	03.11.06*	31.10.06	-2,0d																					▼ S25																	
DS - Delivery Start	09.02.07	09.02.07*	21.02.07	8,0d																																						
M3/ S4	28.03.07	28.03.07*	28.03.07	0,0d																																						
Project: QCT_6250_QCT_6250_Onyx PL	10.11.06	10.11.06		0,0d																																						
M0	23.12.05	09.01.06 A															▼ M0																									
M1	23.03.06	23.03.06*	17.02.06	-24,0d													▼ M1																									
S25	04.07.06	04.07.06*	04.07.06	0,0d																					▼ S25																	
DS - Delivery Start / German Retailer	20.10.06	20.10.06*	20.10.06	0,0d																																						
M3/ S4	10.11.06	10.11.06*	10.11.06	0,0d																																						
Project: Swan Apoxi Rough Planning	11.12.06	08.01.07		-25,0d																																						
M1	10.02.06	24.02.06*	24.02.06	-23,0d													▼ M1																									
S25	19.07.06	25.07.06*	14.07.06	-7,0d																					▼ S25																	
DS - Delivery Start 900MHz EMEA	12.10.06	09.11.06*	10.10.06	-28,4d																																						
M3/S4	11.12.06	11.12.06*	15.12.06	-50,4d																																						
DS - Delivery Start 850MHz LAM	08.12.06	08.01.07*	05.12.06	-23,0d																																						
DS - Delivery Start Chinese	08.12.06	08.01.07*	05.12.06	-23,0d																																						
