

Main Milestone Overview (M0,M1,S25,DS,M3

06.03.06 17:00


◆ = M0/M1 Target ▼ = Current Target --/- = Calculated finish



Main Milestone Overview (M0,M1,S25,DS,M3

06.03.06 17:00

◆ = M0/M1 Target ▼ = Current Target --/- = Calculated finish

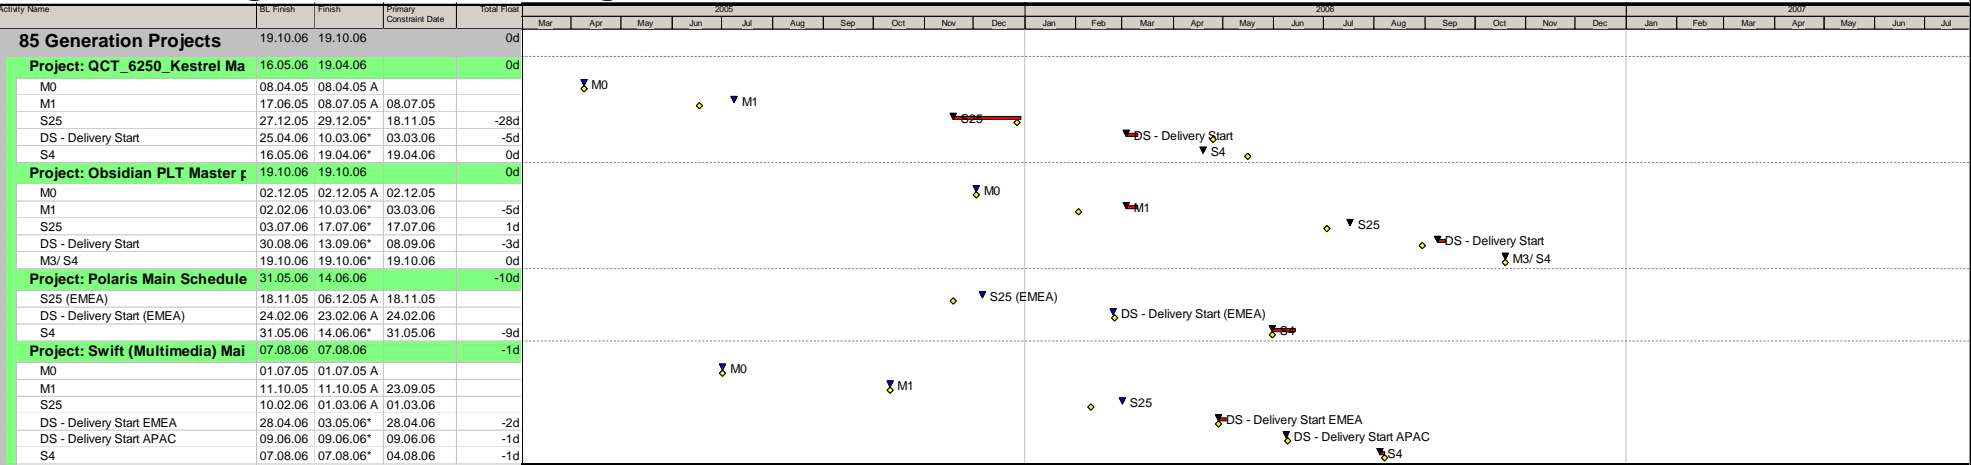

Main Milestone Overview (M0,M1,S25,DS,M3

06.03.06 17:00

◆ = M0/M1 Target ▼ = Current Target --/- = Calculated finish

Activity Name	BL Finish	Finish	Primary Constraint Date	Total Float	2005												2006												2007											
					Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul							
95 Generation Projects	30.03.07	30.03.07		979d																																				
Project: X95_MP-E+_SG3_Dian	30.03.07	30.03.07		0d																																				
M0	17.03.06	17.03.06*	17.03.06	0d																																				
M1	17.05.06	17.05.06*	17.05.06	0d																																				
S25	09.11.06	09.11.06*	09.11.06	0d																																				
DS (EMEA)	23.02.07	23.02.07*	23.02.07	0d																																				
M3/ S4	30.03.07	30.03.07*	30.03.07	0d																																				
Project: Jerry (VF simply) PLT I	04.10.06	04.10.06		1106d																																				
M0	15.03.06	15.03.06		1243d																																				
M1	10.04.06	10.04.06		1225d																																				
S25	12.07.06	12.07.06		1164d																																				
DS - Delivery Start	22.09.06	22.09.06		1112d																																				
M3/ S4	04.10.06	04.10.06		1104d																																				
Project: QCT_6250_Onyx PLT I		21.12.06		-29d																																				
M0		09.01.06 A																																						
M1		16.03.06*	24.02.06	-14d																																				
S25		27.07.06*	04.07.06	-17d																																				
DS - Delivery Start / German Retailer		20.10.06*	20.10.06	0d																																				
M3/ S4		21.12.06*	10.11.06	-29d																																				
