


Main Milestone Overview (M0,M1,S25,DS,M3

27.02.06 17:00


◆ = M0/M1 Target ▼ = Current Target - - / - - = Calculated finish

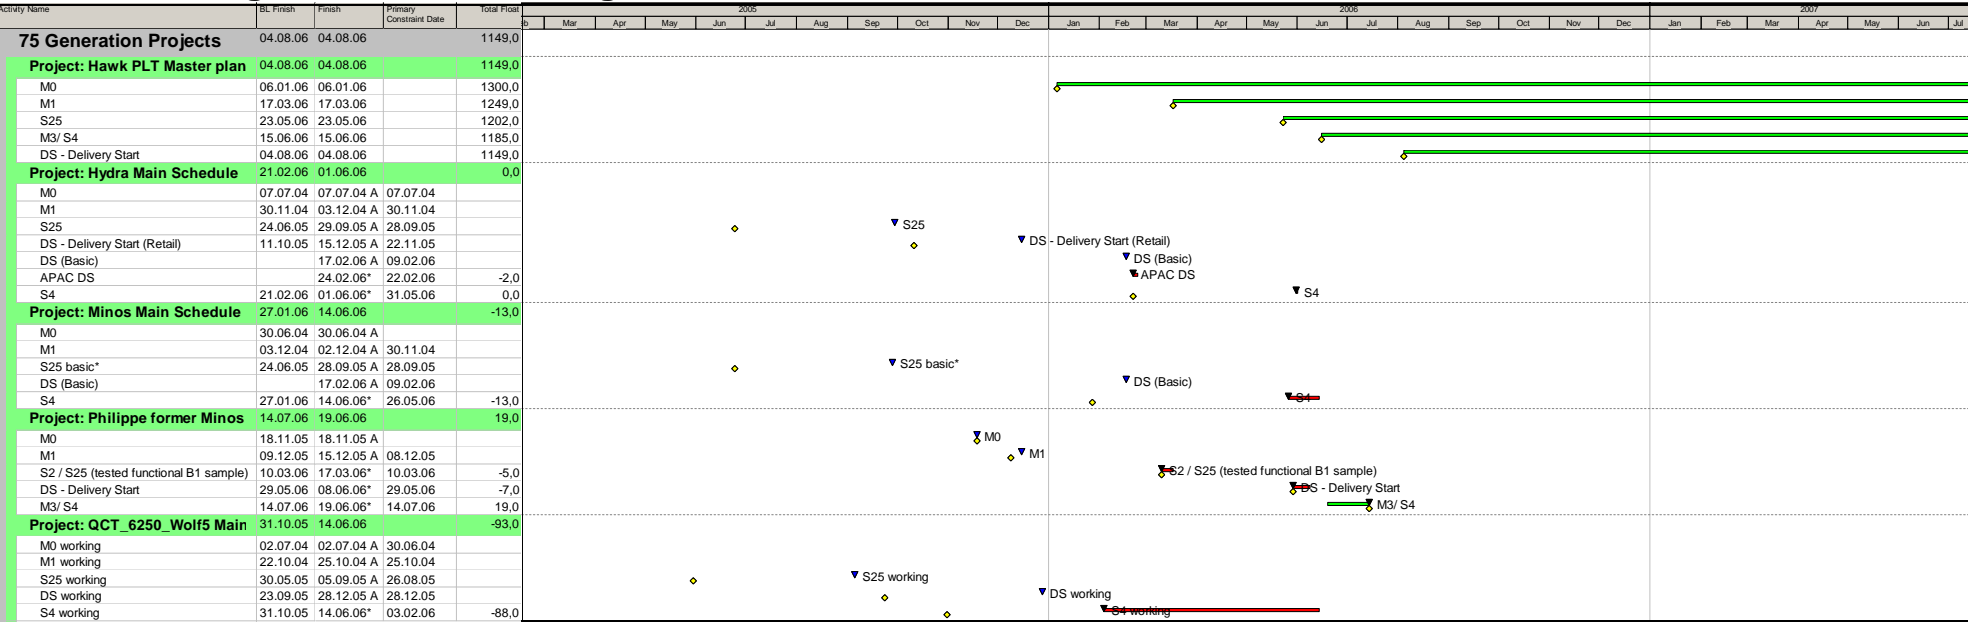

Main Milestone Overview (M0,M1,S25,DS,M3

27.02.06 17:00

◆ = M0/M1 Target ▼ = Current Target --/- = Calculated finish

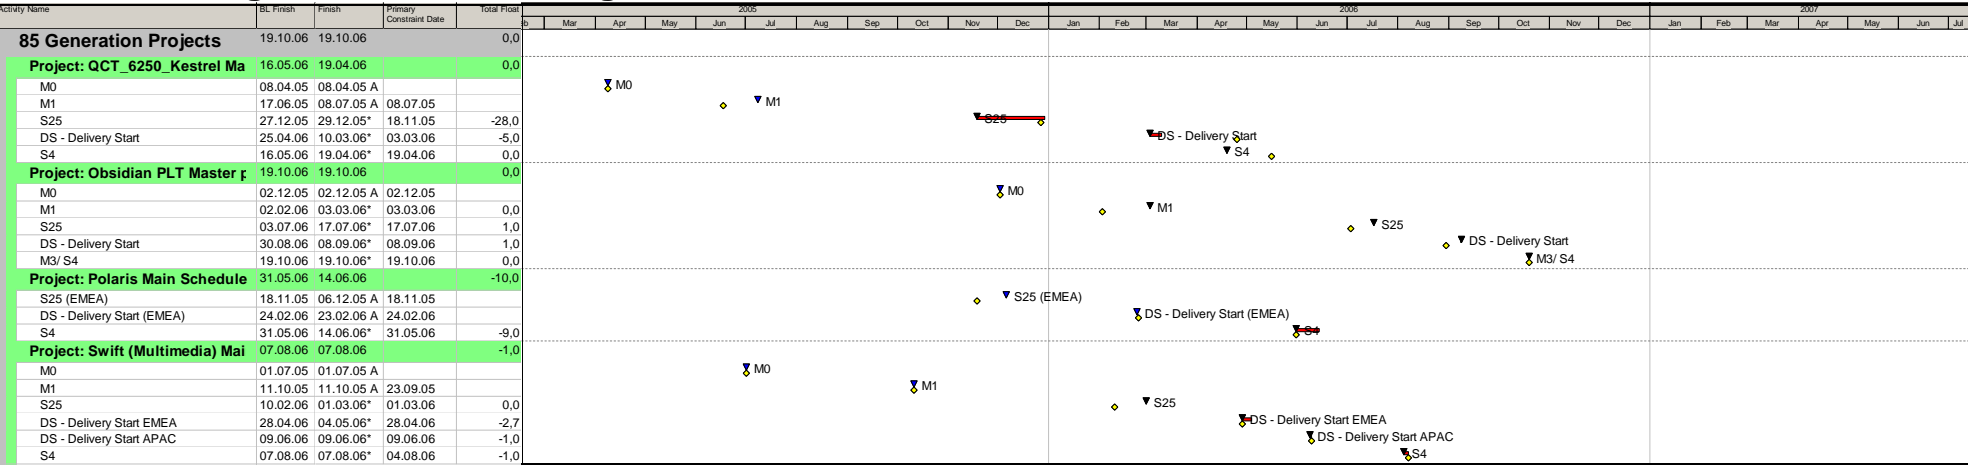

Main Milestone Overview (M0,M1,S25,DS,M3

27.02.06 17:00

◆ = M0/M1 Target ▼ = Current Target --/- = Calculated finish

Activity Name	BC Finish	Finish	Primary Constraint Date	Total Float	2006												2007																					
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul			
95 Generation Projects																																						
Project: X95_MP-E+ SG3_Dian	30.03.07	30.03.07		979,0																																		
M0	08.03.06	08.03.06*	08.03.06	0,0																																		
M1	17.05.06	17.05.06*	17.05.06	0,0																																		
S25	09.11.06	09.11.06*	09.11.06	0,0																																		
DS (EMEA)	23.02.07	23.02.07*	23.02.07	0,0																																		
M3/ S4	30.03.07	30.03.07*	30.03.07	0,0																																		
Project: Jerry (VF simply) PLT I	05.10.06	05.10.06		1105,0																																		
M0	15.03.06	15.03.06		1243,0																																		
M1	31.03.06	31.03.06		1231,0																																		
S25	18.07.06	18.07.06		1160,0																																		
DS - Delivery Start	22.09.06	22.09.06		1112,0																																		
M3/ S4	05.10.06	05.10.06		1103,0																																		
Project: QCT_6250_Onyx PLT I		21.12.06		-29,0																																		
M0		09.01.06 A																																				
M1		16.03.06*	24.02.06	-14,0																																		
S25		27.07.06*	04.07.06	-17,0																																		
DS - Delivery Start / German Retailer		20.10.06*	20.10.06	0,0																																		
M3/ S4		21.12.06*	10.11.06	-29,0																																		
