

U2 Status - Swift

Dr. Markus Jäger / Thomas Hien


BenQ Mobile PHE RD SWM PL

Munich/Kamp-Lintfort, March 1st, 2006

BenQ


Swift – defect trends

(Prio 1 defects - RPN > 1000 and optimistic value - without defects in test)

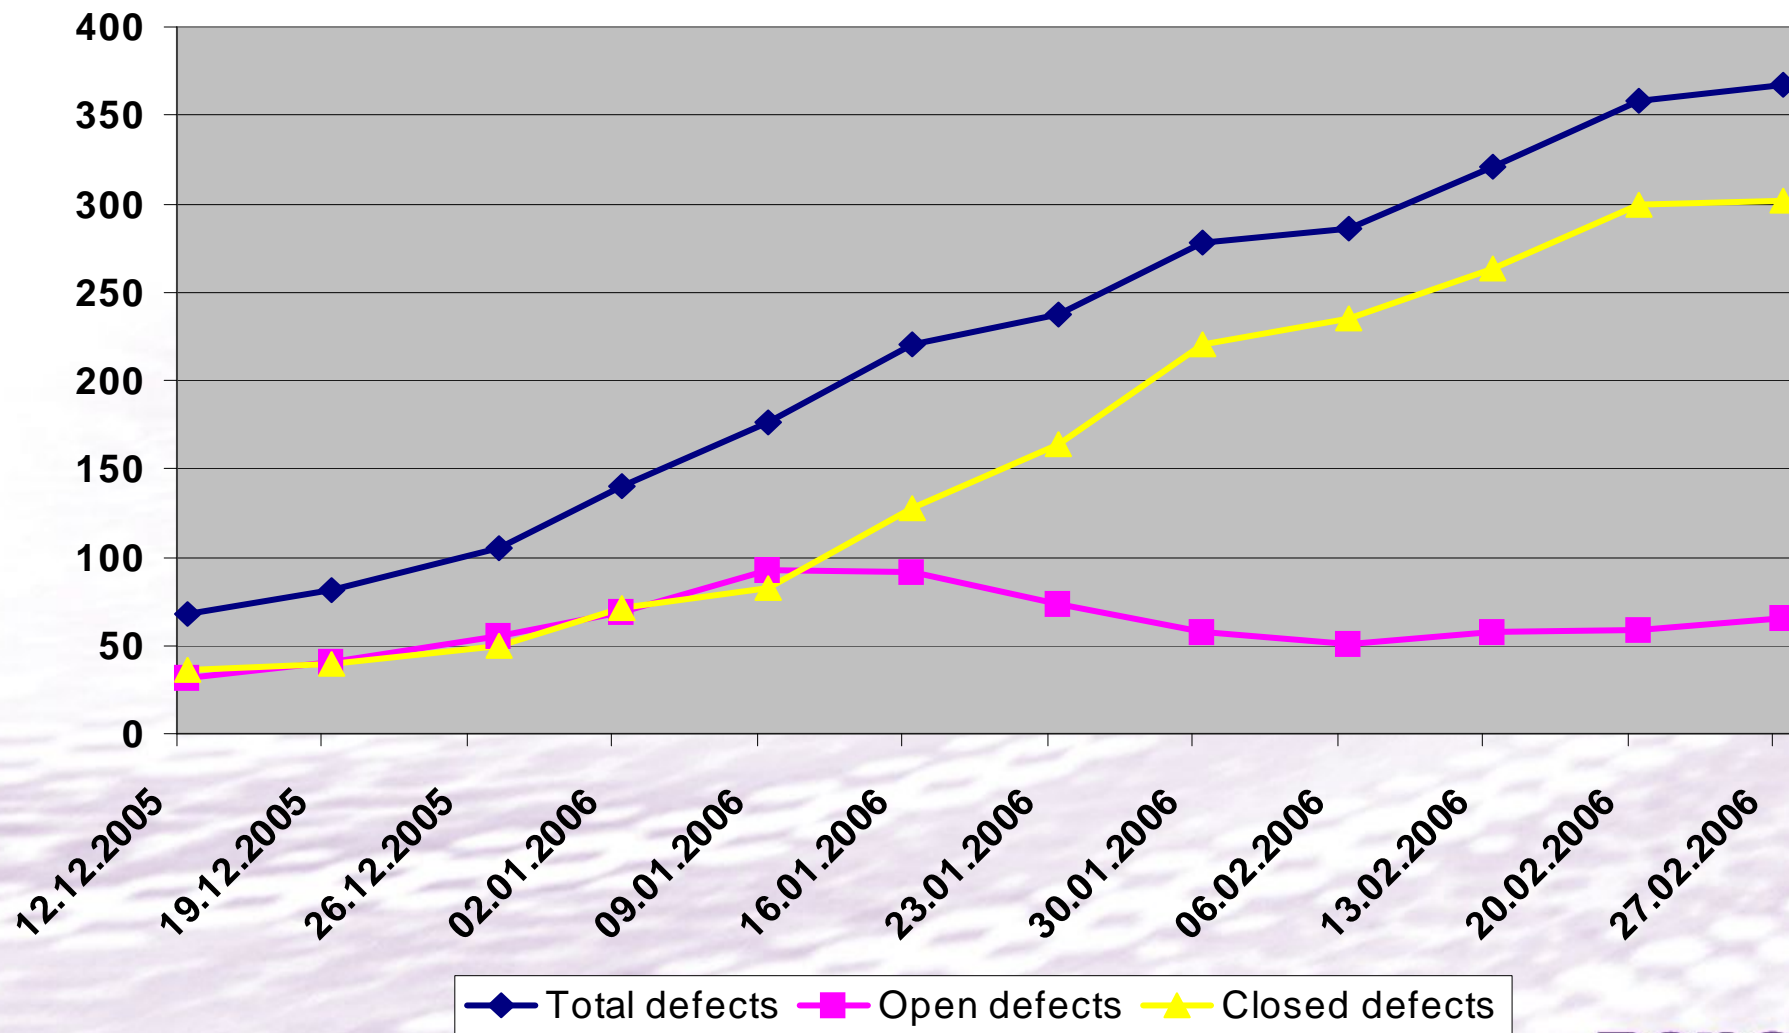


Swift – risk customer claims/returns trend

(optimistic nCCPI value – without defects in test)

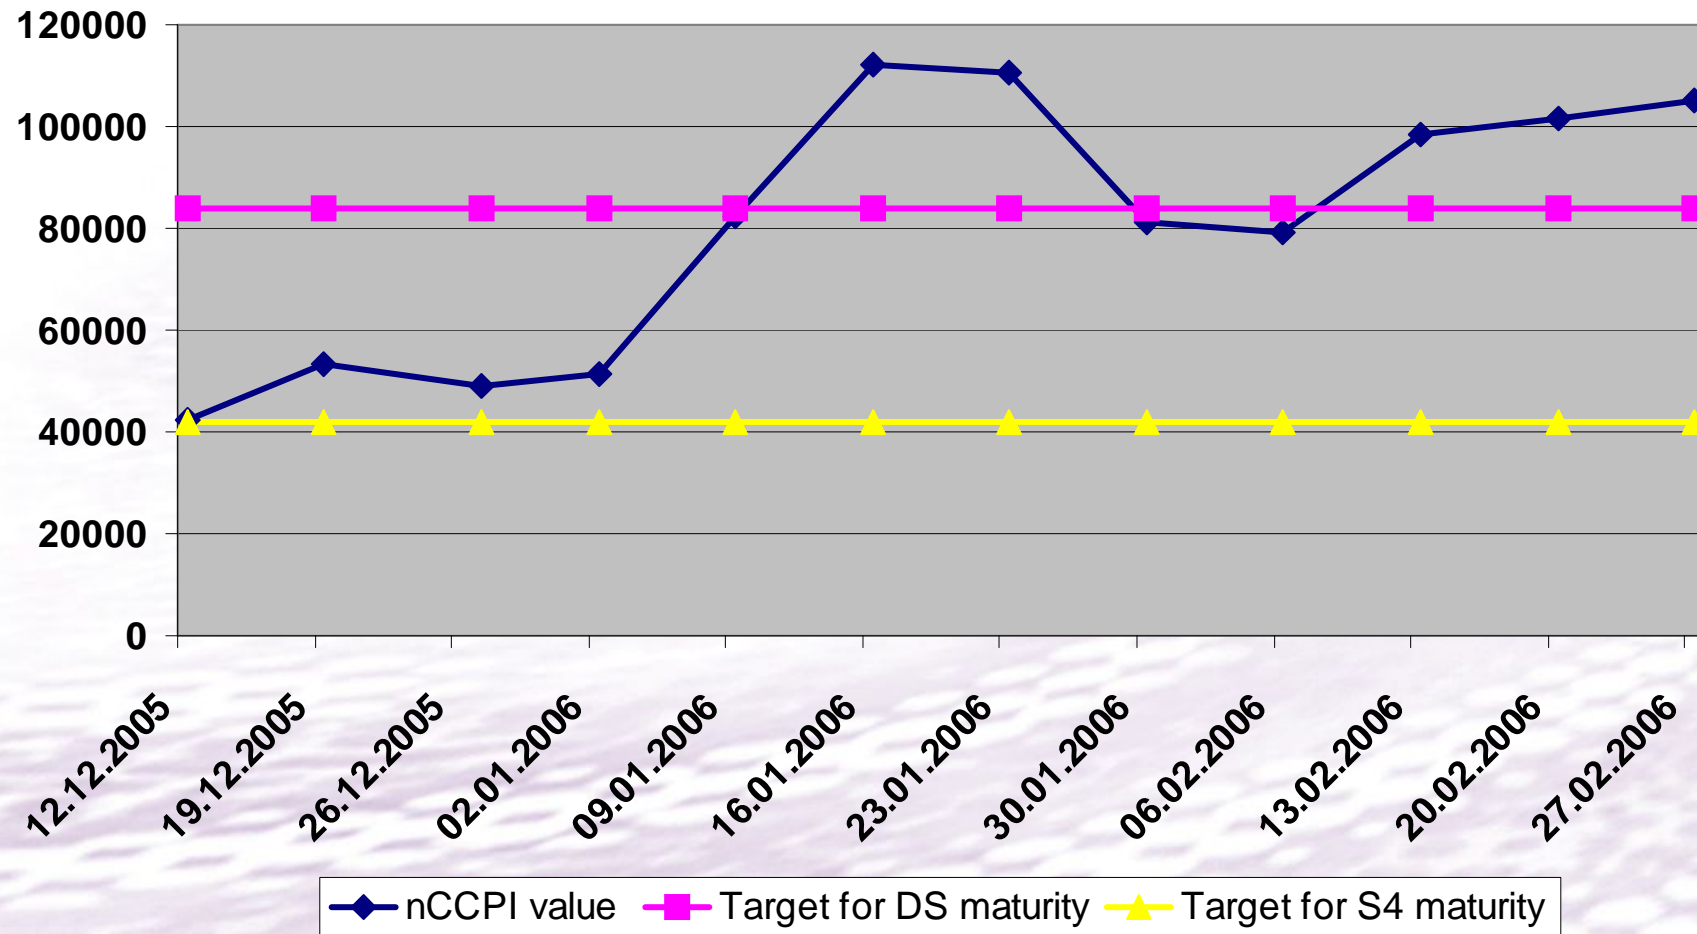


Swift – historical trends prio 1 defects (S3)

Optimistic defects (without defects in test)

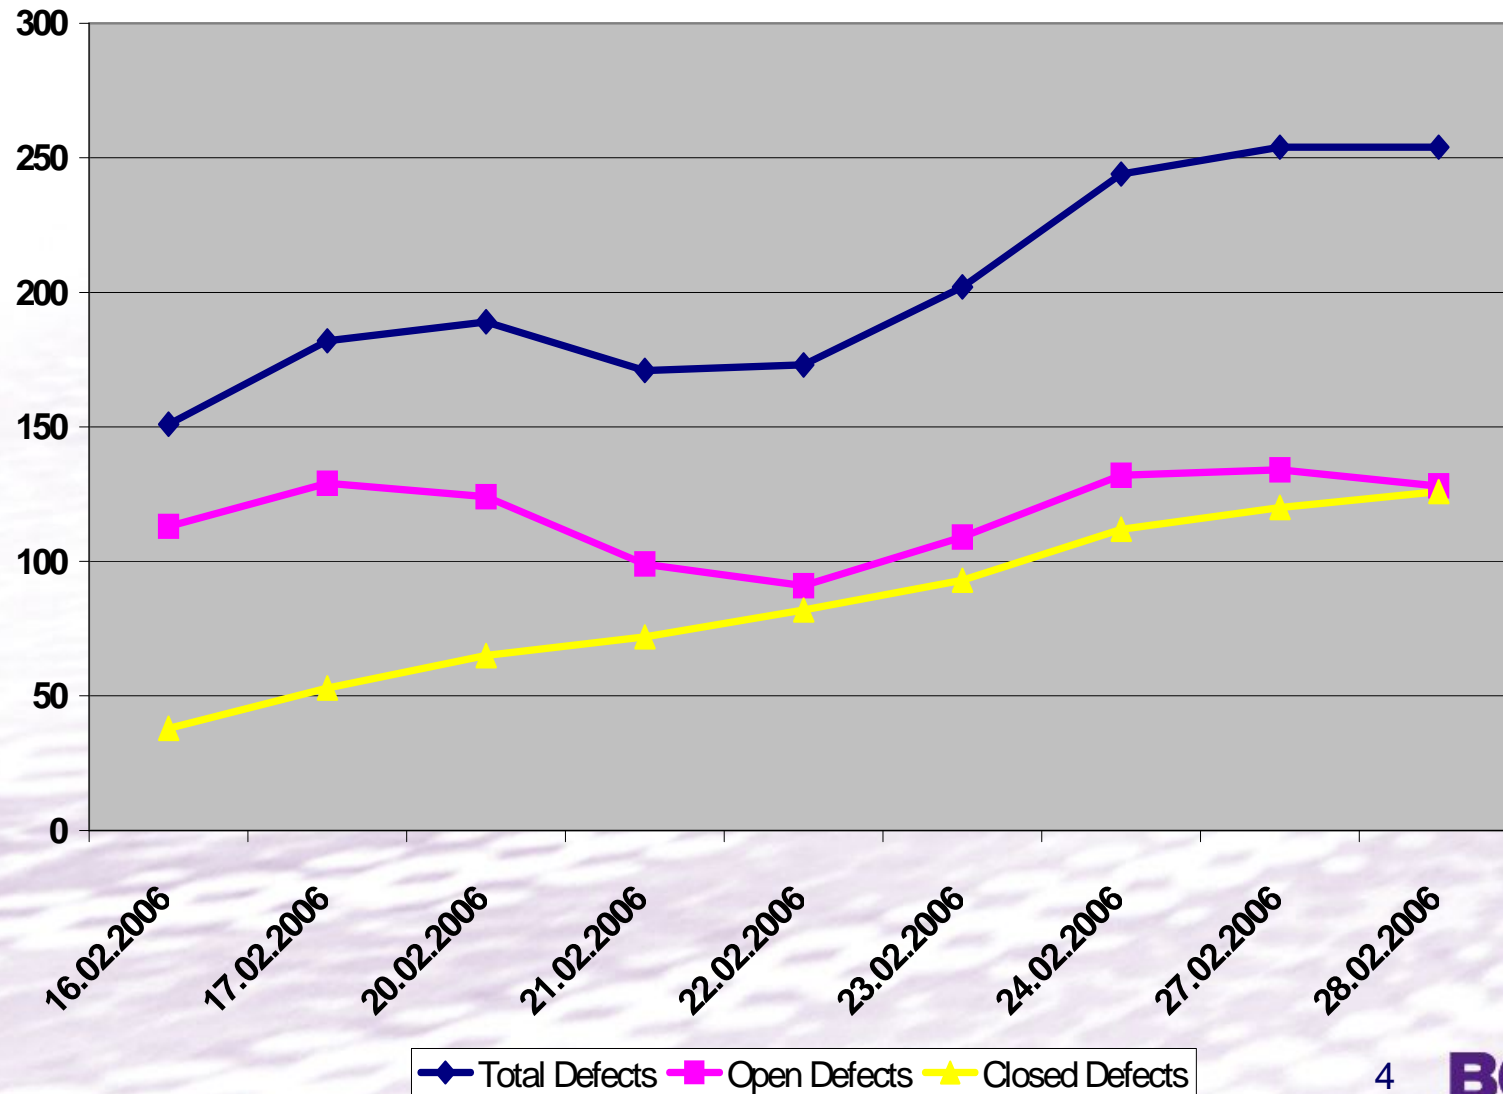

Swift – historical trends S3 defects

Optimistic defects (without defects in test)

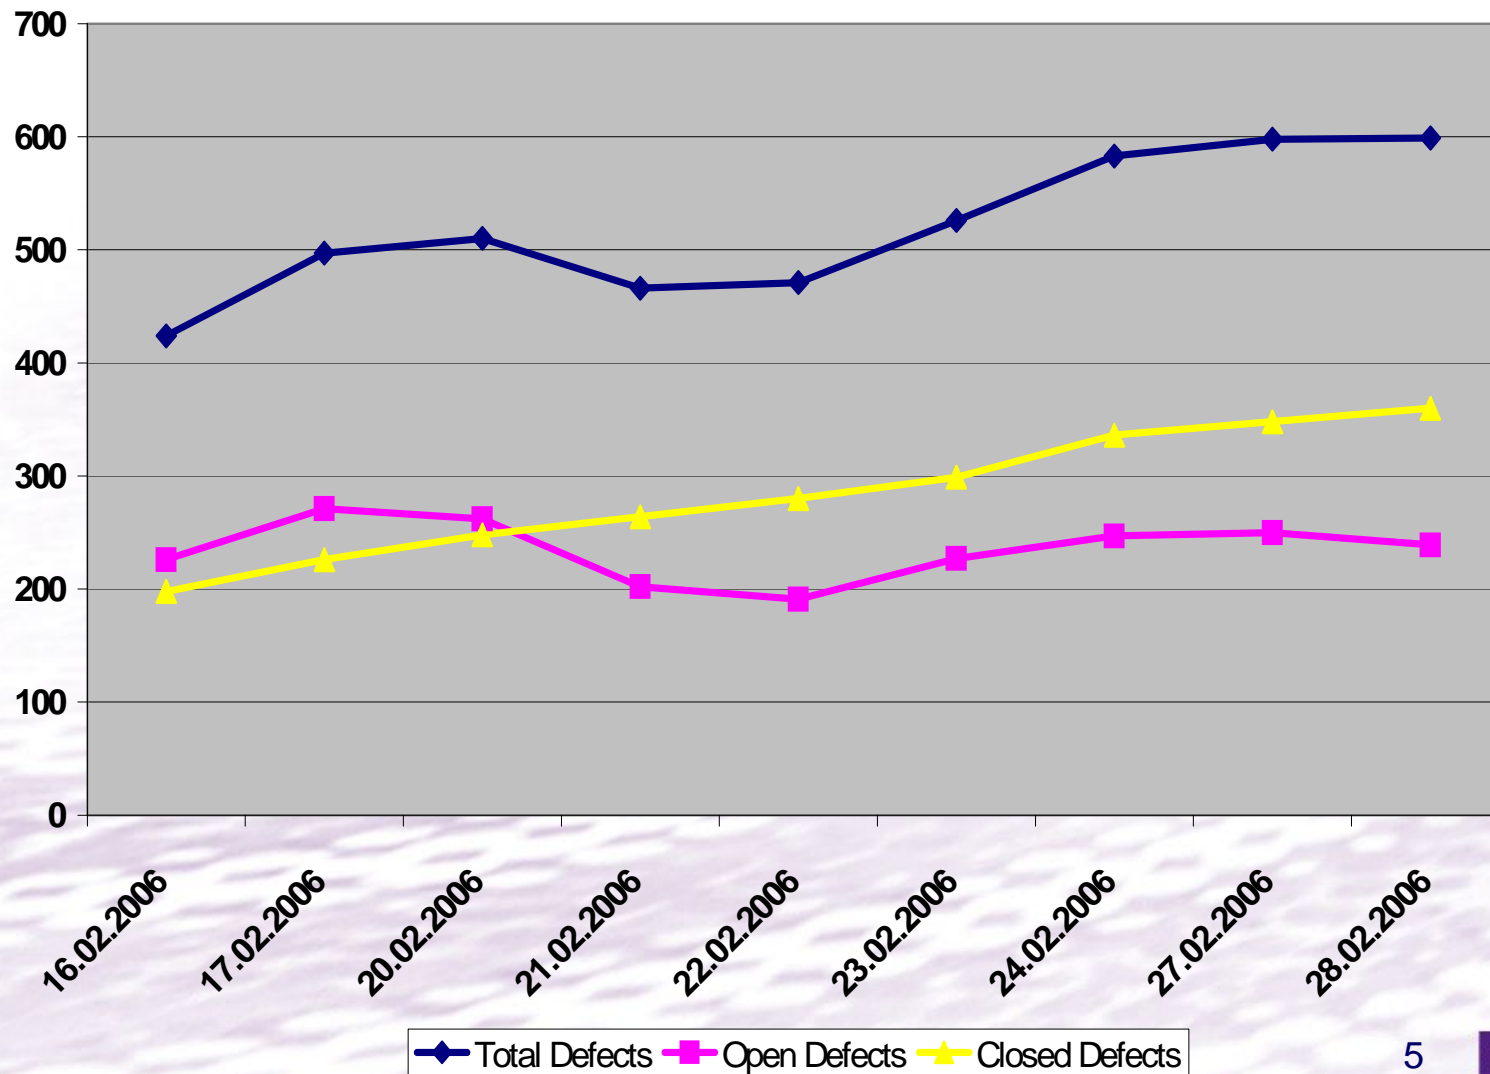


Swift – Milestone Overview

	Step 1	Step 2 (incl. Fasttrack)
M0	01.07.2005	
S0	10.10.2005	
M1	10.10.2005	
S15	10.10.2005	
S2	26.10.2005	
S25	03.02.2006	planned for 10.03.2006 currently delayed to 24.03.2006 (*)
AS	03.03.2006 (Currently being declared)	planned for 31.03.2006
S3	planned for 31.03.2006 risk in the area of streaming (**)	planned for 05.05.2006
DS	planned for 28.04.2006	planned for 09.06.2006
S4	planned for 04.08.2006	


(*) High number of technical problems to get Fasttrack up and running

(**) Not yet fully running on Minos (base for Swift); high number of open defects; same team as for Fasttrack (some resource have currently been shifted to get Fasttrack up and running)

Swift – feature Streaming

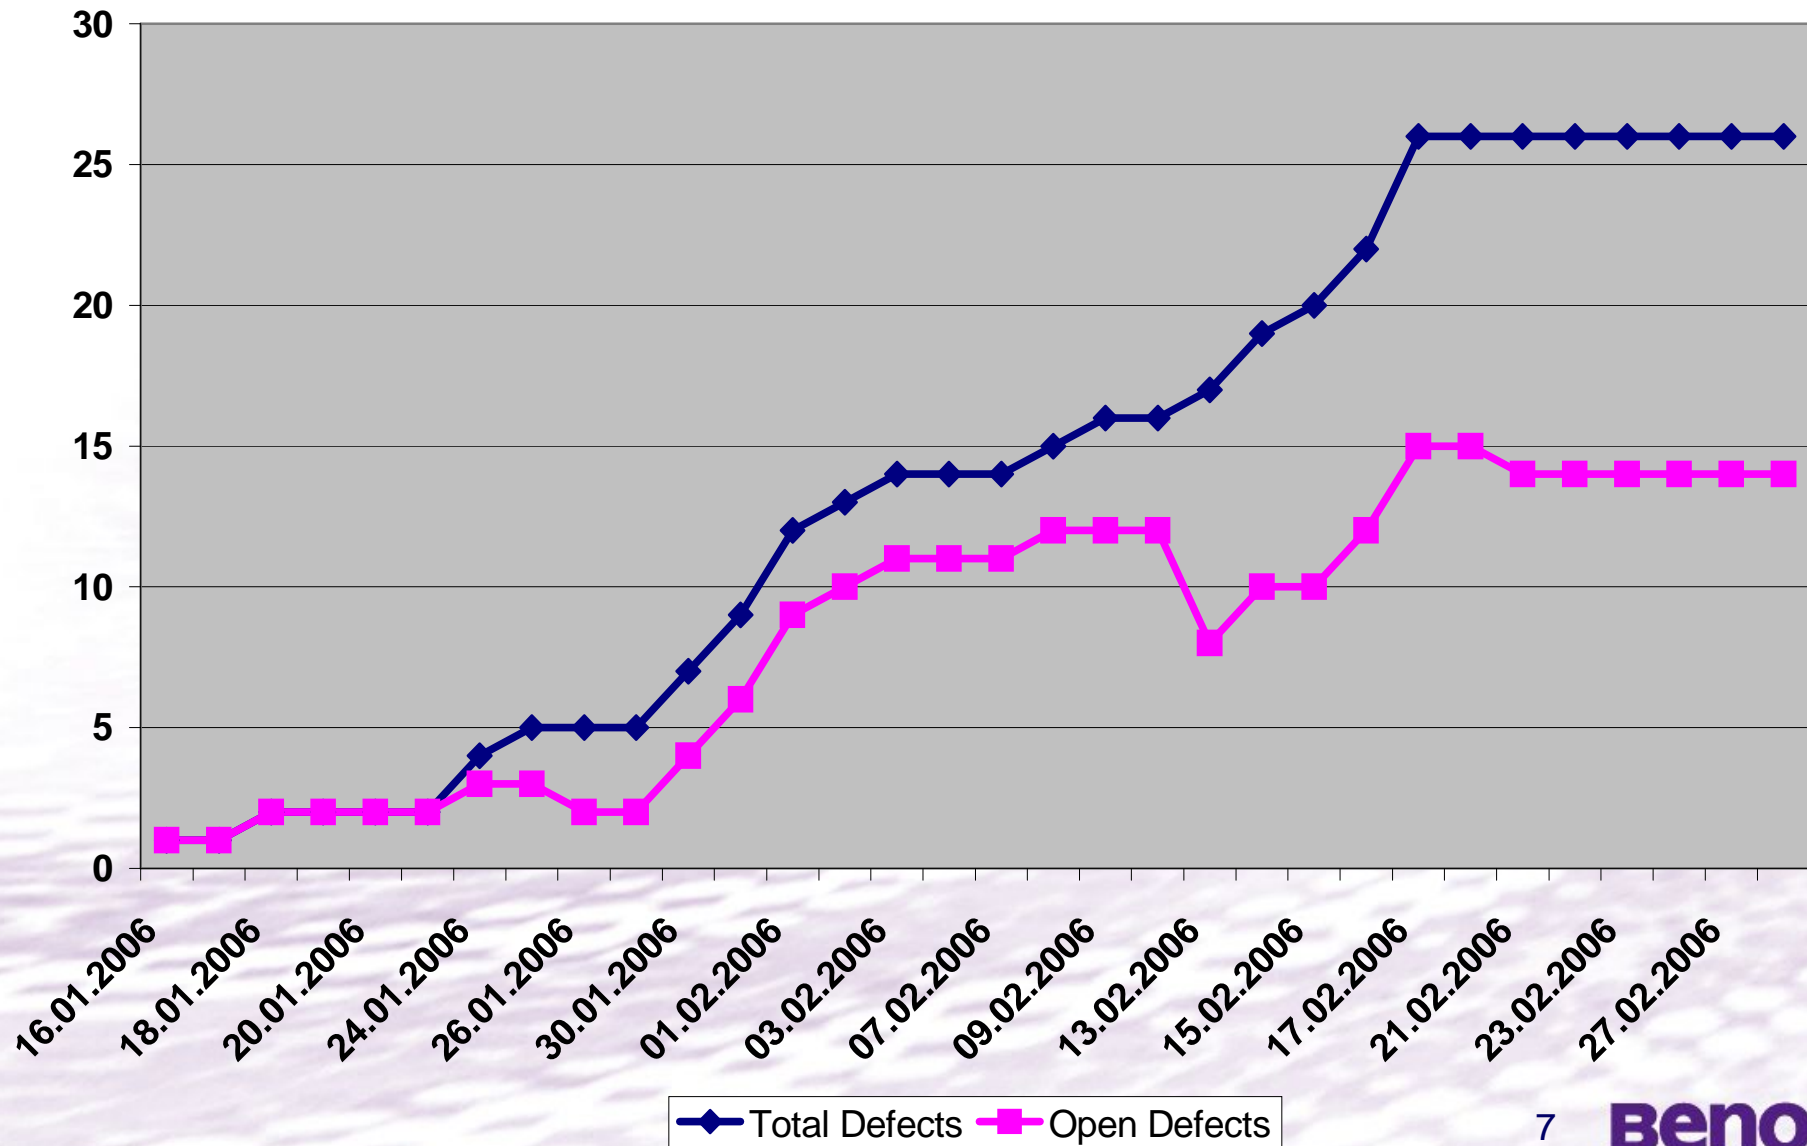


Swift – defect trends critical components

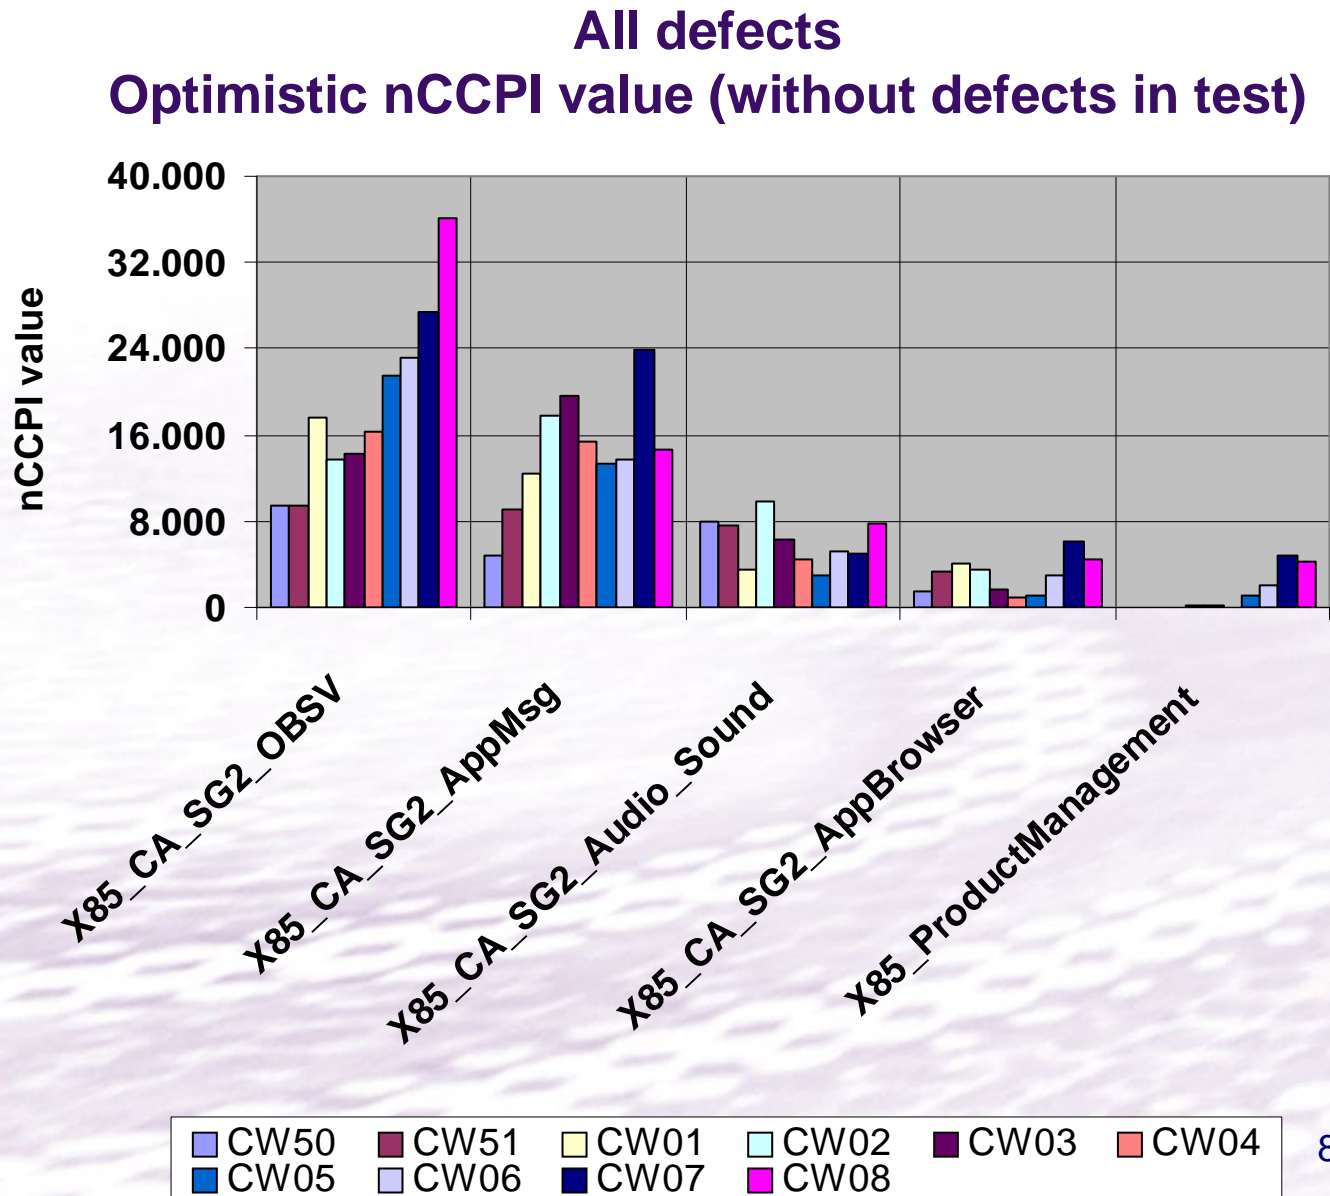


Swift – defect trends critical components

Prio 1 defects (\approx RPN >1000)

Optimistic value (without defects in test)

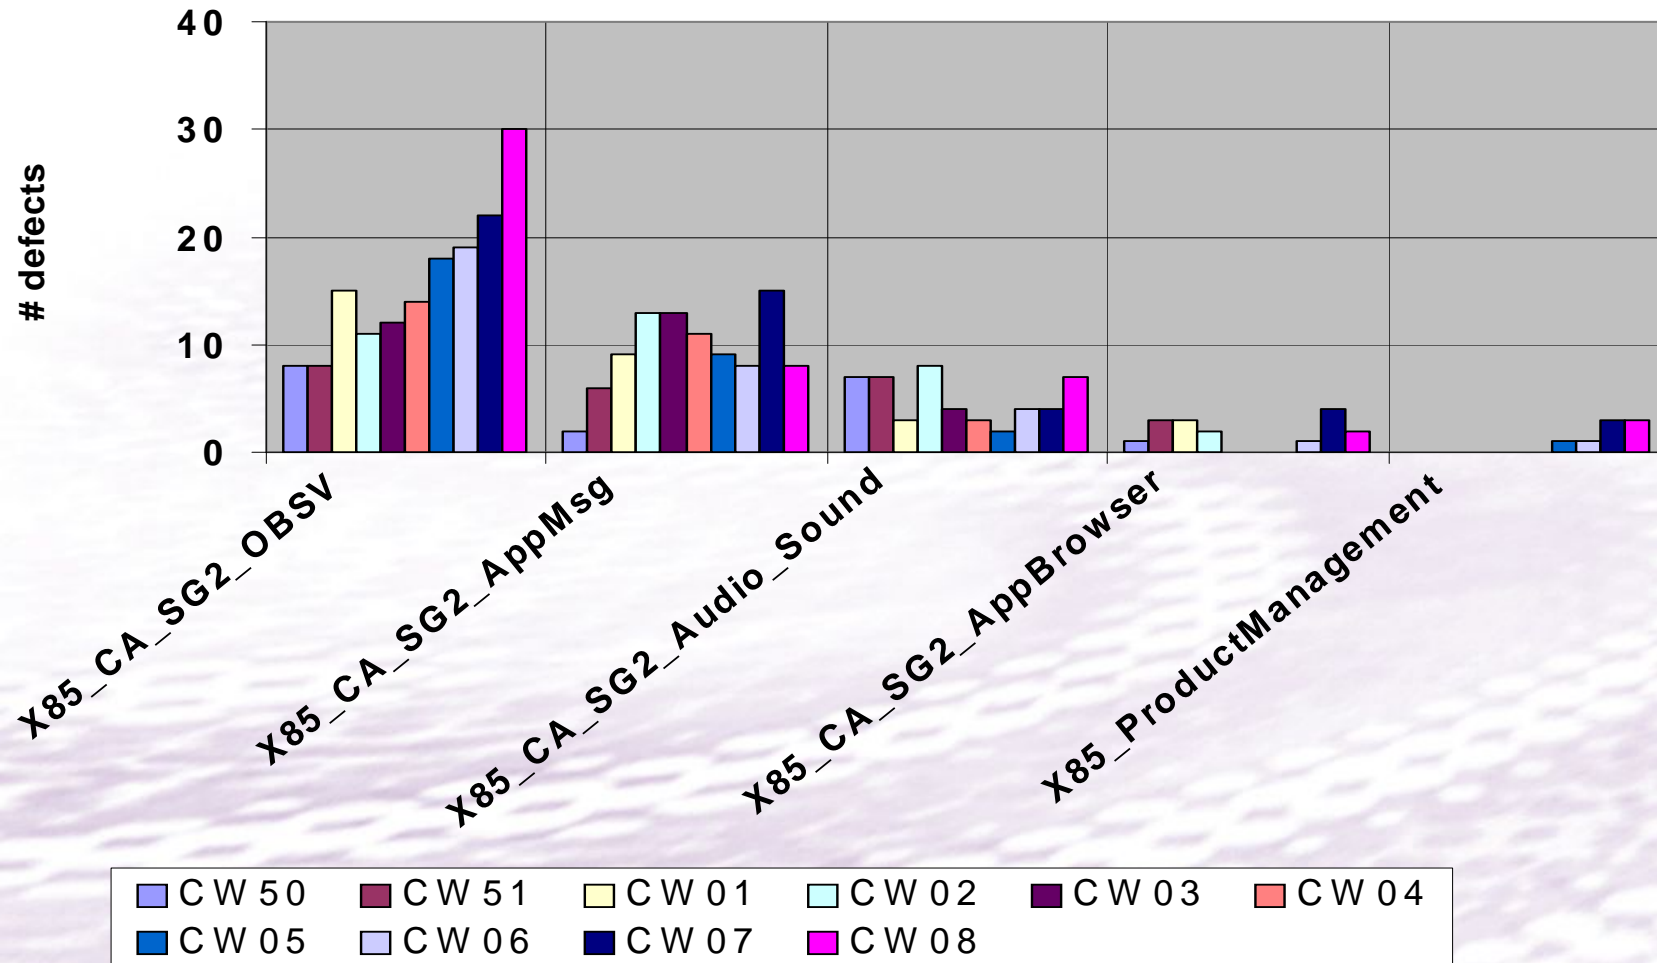

Swift – test coverage and pass rate (S3 run)

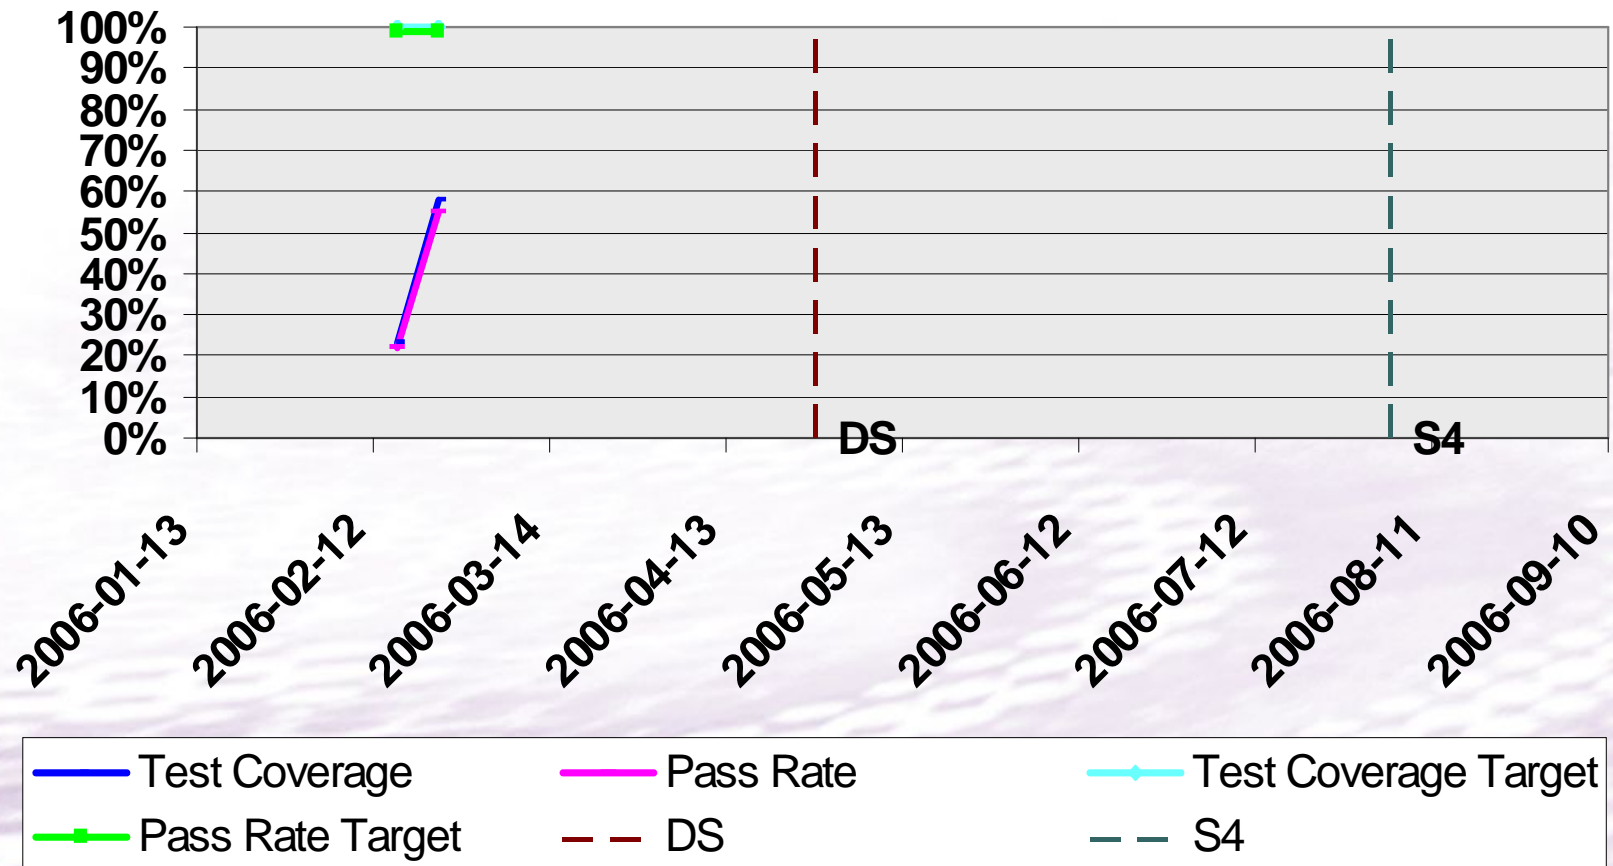

Swift – shopping list (top 8 components)

Component	SR1 (15.02.-28.02.06)		
	planned	Actual	Ratio
X85_CA_SG2_AppBrowser	6	2	66,67%
X85_CA_SG2_AppIdc	8	0	100,00%
X85_CA_SG2_AppMMUI	6	0	100,00%
X85_CA_SG2_AppMsg	16	1	93,75%
X85_CA_SG2_AppPim	10	0	100,00%
X85_CA_SG2_IMPS	7	1	85,71%
X85_CA_SG2_JavaApps	9	0	100,00%
X85_CA_SG2_UI-Customization	6	1	83,33%
Other	19	4 (*10)	63,16%
Total	87 (*93)	9 (*15)	86,67%

Swift – shopping list SR1

